


001.0 February Update Logan Ave Type B Schedule..mpp

ID	Uniqu ID	Task Name	Duration	Start	Actual Start	Finish	Actual Finish	Total Slack	1 October 1	November 1	December 1	January 1	February 1	March 1	April 1	May 1	June 1	July 1	August 1	September 1	October 1
111	215	Electrical	98 days	Mon 1/11/16	Mon 1/11/16	Mon 6/6/16	NA	25 days													
112	275	Install Illumination Conduit/Boxes	0 days	Tue 2/16/16	Tue 2/16/16	Mon 2/29/16	Mon 2/29/16	0 days													
113	276	Install Interconnect Conduit	23 days	Tue 2/16/16	Tue 2/16/16	Thu 3/17/16	Thu 3/17/16	0 days													
114	277	Install Illumination Foundations	16 days	Fri 3/18/16	NA	Fri 4/8/16	NA	15 days													
115	217	Illumination Poles	15 days	Mon 5/2/16	NA	Fri 5/20/16	NA	0 days													
116	433	Illumination Complete	0 days	Fri 5/20/16	NA	Fri 5/20/16	NA	0 days													
117	274	Install interconnect	10 days	Mon 3/7/16	Mon 3/7/16	Mon 6/6/16	NA	25 days													
118	380	Electric Lightwave	20 days	Tue 2/16/16	Tue 2/16/16	Mon 3/14/16	NA	22 days													
119	381	Trench and Conduit	15 days	Tue 2/16/16	Tue 2/16/16	Mon 3/7/16	Mon 3/7/16	0 days													
120	410	Electric Lightwave install fiber	5 days	Mon 3/7/16	Mon 3/7/16	Mon 3/14/16	NA	22 days													
121	382	Zayo	18 days	Tue 2/16/16	Tue 2/16/16	Thu 3/10/16	NA	86 days													
122	383	Zayo Trench and conduit	15 days	Tue 2/16/16	Tue 2/16/16	Mon 3/7/16	Mon 3/7/16	0 days													
123	411	Zayo Install Fiber	3 days	Mon 3/7/16	Mon 3/7/16	Thu 3/10/16	NA	86 days													
124	384	Interconnect	15 days	Tue 2/16/16	Tue 2/16/16	Mon 3/7/16	Mon 3/7/16	0 days													
125	385	Trench and Conduit	15 days	Tue 2/16/16	Tue 2/16/16	Mon 3/7/16	Mon 3/7/16	0 days													
126	333	Project Suspension	0 days	Thu 1/14/16	NA	Thu 1/14/16	NA	119 days													
127	334	Review Weather Conditions and TESC Before Proceeding	0 days	Thu 1/14/16	NA	Thu 1/14/16	NA	110 days													
128	265	Demolition	9 days	Mon 1/11/16	Mon 1/11/16	Fri 1/29/16	Fri 1/29/16	0 days													
129	190	Clearing and Grubbing for Road Construction	0 days	Mon 1/11/16	Mon 1/11/16	Thu 1/14/16	Thu 1/14/16	0 days													
130	198	Demo East Logan Ave N Centerline	9 days	Mon 1/18/16	Mon 1/18/16	Fri 1/29/16	Fri 1/29/16	0 days													
131	197	Roadway Reconstruction	57 days	Mon 1/18/16	Mon 1/18/16	Thu 4/14/16	NA	51 days													
132	199	Complete Stage 1 Roadway Excavation	9 days	Mon 1/18/16	Mon 1/18/16	Fri 1/29/16	Fri 1/29/16	0 days													
133	194	Place Crushed Rock Base and Grade for HMA	8 days	Tue 3/8/16	NA	Thu 3/17/16	NA	-9 days													
134	195	Install Curb on the East Side Of Logan Ave	3 days	Fri 3/18/16	NA	Tue 3/22/16	NA	-9 days													
135	165	Base Pave Logan Ave Stage 1	3 days	Wed 3/23/16	NA	Fri 3/25/16	NA	-9 days													
136	339	Grade for Lightside Concrete	4 days	Wed 3/23/16	NA	Mon 3/28/16	NA	63 days													
137	266	Cement Conc. Traffic Curb and Gutter	2 days	Mon 3/28/16	NA	Tue 3/29/16	NA	-9 days													
138	267	Cement Conc. Traffic Curb	1 day	Wed 3/30/16	NA	Wed 3/30/16	NA	-9 days													
139	268	Cement Conc. Pedestrian Curb	1 day	Thu 3/31/16	NA	Thu 3/31/16	NA	-9 days													
140	269	Cement Concrete Driveway Entrance	2 days	Fri 4/1/16	NA	Mon 4/4/16	NA	-9 days													
141	270	Decorative Cement Concrete Sidewalk	6 days	Tue 4/5/16	NA	Tue 4/12/16	NA	-9 days													
142	271	Cement Conc Curb Ramp Type B	1 day	Wed 4/13/16	NA	Wed 4/13/16	NA	-9 days													
143	68	Property Restoration	1 day	Thu 4/14/16	NA	Thu 4/14/16	NA	51 days													
144	343	Boeing Parking Lot work	65 days	Fri 1/8/16	Fri 1/8/16	Mon 4/18/16	NA	59 days													
145	344	High Visibility Fence	1 day	Fri 1/8/16	Fri 1/8/16	Fri 1/15/16	Fri 1/15/16	0 days													
146	345	Sawcut Demo Limits	2 days	Thu 1/14/16	Thu 1/14/16	Fri 1/15/16	Fri 1/15/16	0 days													
147	346	Demo Parking lot	1 day	Fri 1/15/16	Fri 1/15/16	Fri 1/15/16	Fri 1/15/16	0 days													
148	347	Boeing Electrical	11 days	Wed 3/30/16	NA	Wed 4/13/16	NA	59 days													
149	348	Install Conduit	3 days	Wed 3/30/16	NA	Fri 4/1/16	NA	50 days													
150	349	Install Light Bases	3 days	Mon 4/4/16	NA	Wed 4/6/16	NA	50 days													

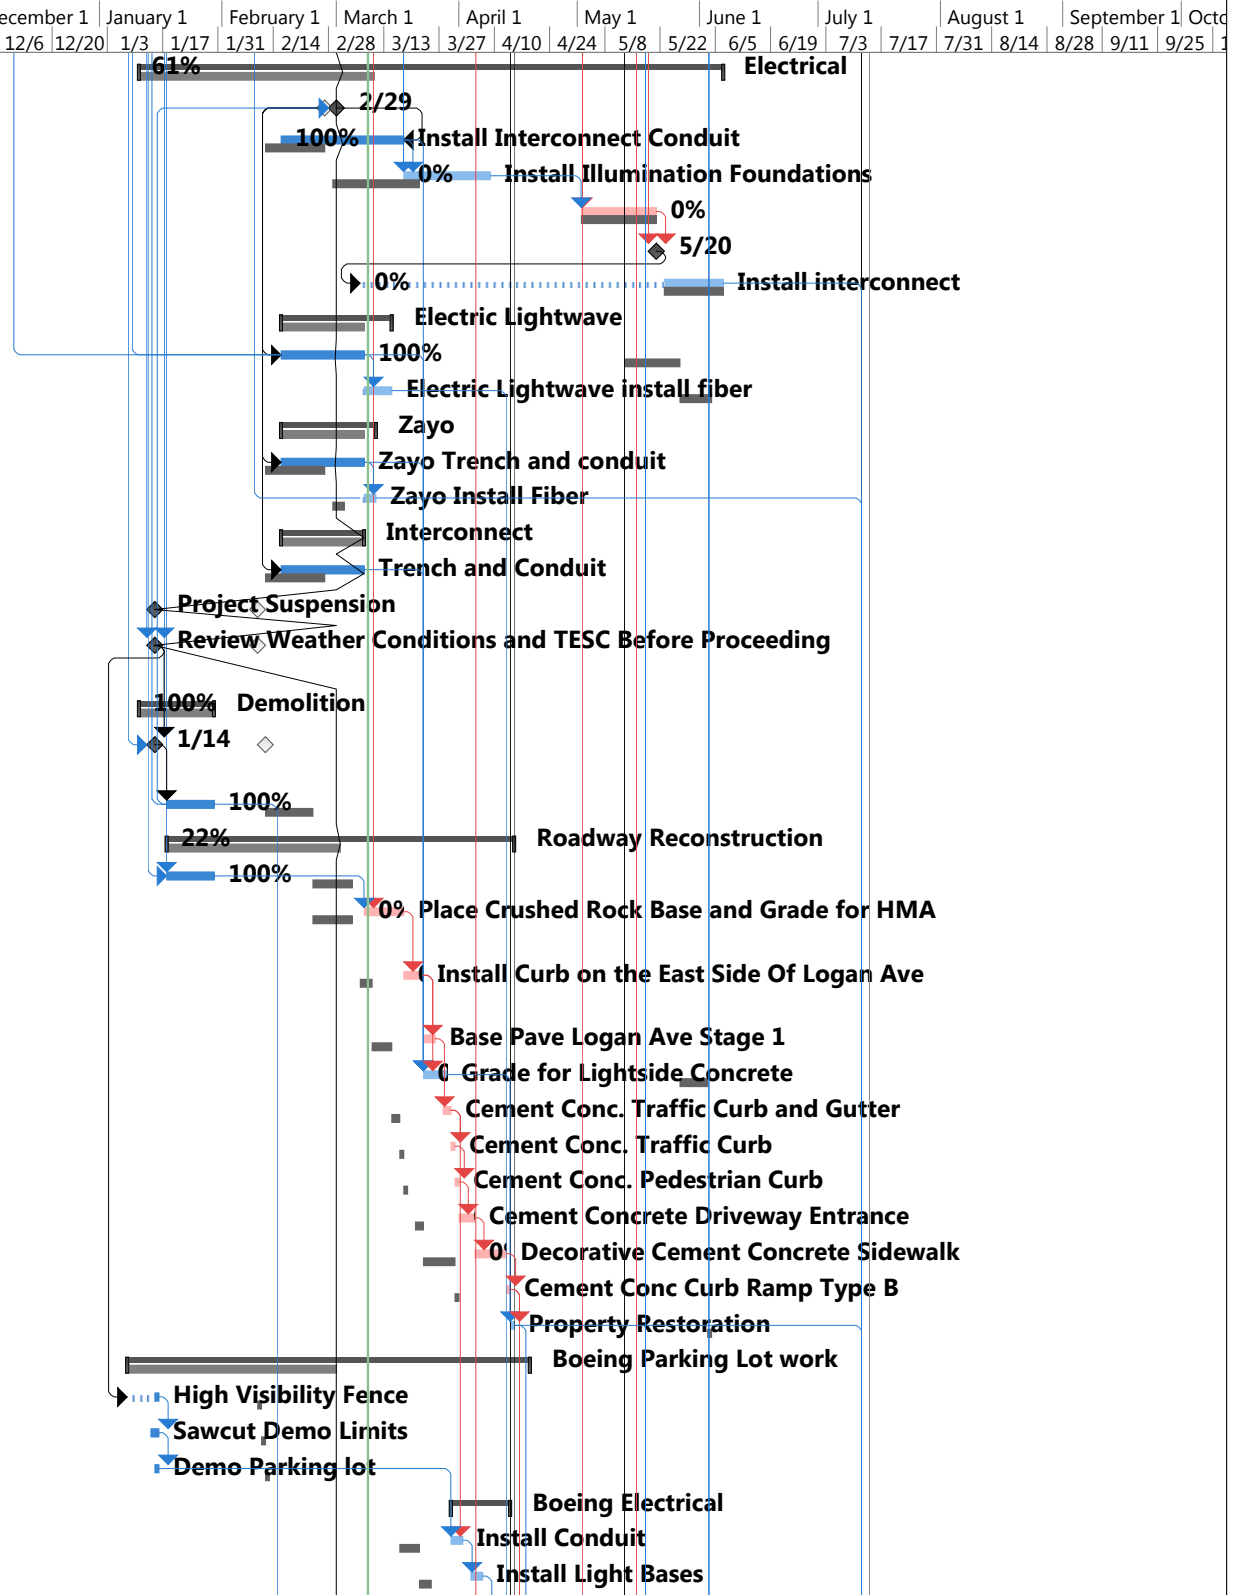


Contact No. TA 4951

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	

001.0 February Update Logan Ave Type B Schedule..mpp

ID	Uniqu ID	Task Name	Duration	Start	Actual Start	Finish	Actual Finish	Total Slack	1 October 1	November 1	December 1	January 1	February 1	March 1	April 1	May 1	June 1	July 1	August 1	September 1	October 1																	
									9/27	10/11	10/25	11/8	11/22	12/6	12/20	1/3	1/17	1/31	2/14	2/28	3/13	3/27	4/10	4/24	5/8	5/22	6/5	6/19	7/3	7/17	7/31	8/14	8/28	9/11	9/25	10/9		
193	393	Install Power Service Cabinet	1 day	Fri 5/13/16	NA	Fri 5/13/16	NA	29 days																														
194	396	Install Signal Cabinet	1 day	Wed 6/1/16	NA	Wed 6/1/16	NA	18 days																														
195	207	Traffic Signal System @ N 3rd Street, Complete	1 day	Thu 6/2/16	NA	Thu 6/2/16	NA	18 days																														
196	404	N 4th Street Signal System	25 days	Thu 4/28/16	NA	Thu 6/2/16	NA	27 days																														
197	397	Install Conduit and Foundations	10 days	Thu 4/28/16	NA	Wed 5/11/16	NA	23 days																														
198	398	Install Controller and Service Foundations	2 days	Thu 5/12/16	NA	Fri 5/13/16	NA	23 days																														
199	399	Install Poles and Signal Equipment	5 days	Mon 5/16/16	NA	Fri 5/20/16	NA	23 days																														
200	400	Install Power Service Cabinet	1 day	Mon 5/23/16	NA	Mon 5/23/16	NA	23 days																														
201	401	Install Signal Cabinet	1 day	Wed 6/1/16	NA	Wed 6/1/16	NA	18 days																														
202	208	Traffic Signal System @ N 4th Street, Complete	1 day	Thu 6/2/16	NA	Thu 6/2/16	NA	18 days																														
203	221	Pavement Finishing's	11 days	Mon 6/27/16	NA	Wed 7/13/16	NA	0 days																														
204	103	Planing Bituminous Pavement	1 day	Mon 6/27/16	NA	Mon 6/27/16	NA	0 days																														
205	238	Project Final Lift	2 days	Tue 6/28/16	NA	Wed 6/29/16	NA	0 days																														
206	72	Extruded Curb	1 day	Thu 6/30/16	NA	Thu 6/30/16	NA	0 days																														
207	74	Raised Pavement Marker Type 1	0.5 days	Fri 7/1/16	NA	Fri 7/1/16	NA	0 days																														
208	75	Remove and Replace Monument, Monument Case, and Co	0.5 days	Fri 7/1/16	NA	Fri 7/1/16	NA	0 days																														
209	84	Permanent Signing	1 day	Wed 7/6/16	NA	Wed 7/6/16	NA	0 days																														
210	85	Plastic Line	1 day	Thu 7/7/16	NA	Thu 7/7/16	NA	0 days																														
211	86	Plastic Stop Line	1 day	Fri 7/8/16	NA	Fri 7/8/16	NA	0 days																														
212	87	Plastic Crosswalk Line	1 day	Mon 7/11/16	NA	Mon 7/11/16	NA	0 days																														
213	88	Plastic Traffic Arrow	1 day	Tue 7/12/16	NA	Tue 7/12/16	NA	0 days																														
214	89	Painted Curb	1 day	Wed 7/13/16	NA	Wed 7/13/16	NA	0 days																														
215	200	Request Substantial Completion	0 days	Wed 7/13/16	NA	Wed 7/13/16	NA	0 days																														

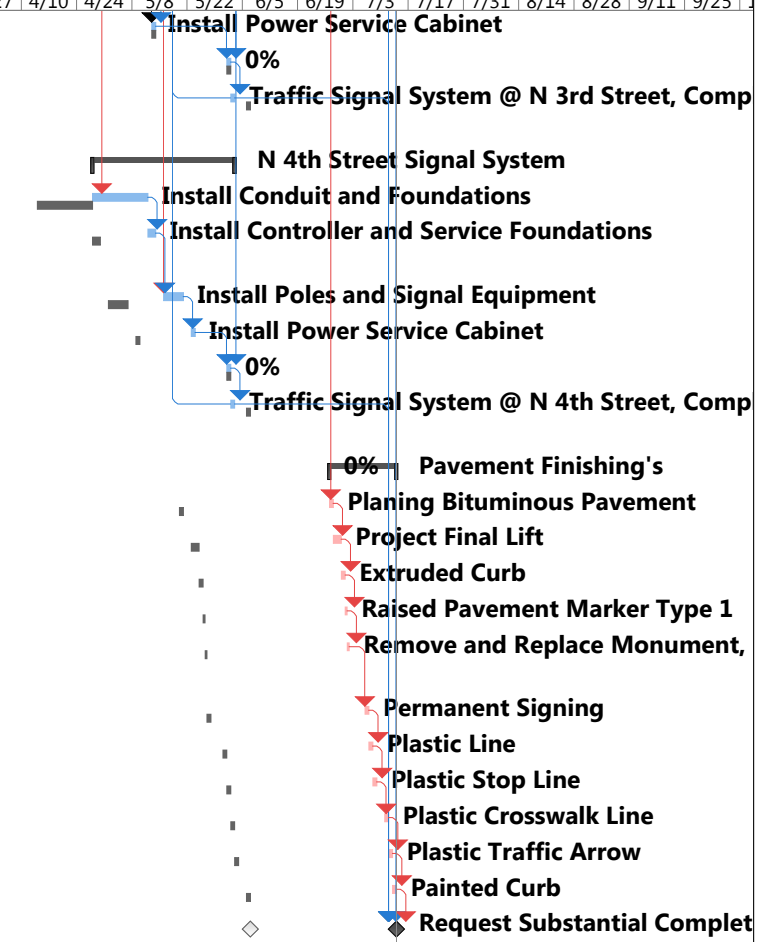

Contact No. TA 4951

Critical		Split		Finish-only		Baseline Milestone		Manual Summary		Inactive Task	
Critical Split		Task Progress		Duration-only		Milestone		Project Summary		Inactive Milestone	
Critical Progress		Manual Task		Baseline		Summary Progress		External Tasks		Inactive Summary	
Task		Start-only		Baseline Split		Summary		External Milestone		Deadline	
