


Contact No. TA 4951

█ Critical Progress
 █ Split
 █ Manual Task
 █ Finish-only
 █ Baseline
 █ Baseline Milestone
 █ Summary Progress
 █ Manual Summary
 █ External Tasks
 █ Inactive Task
 █ Inactive Summary
 █ Critical Split
 █ Task
 █ Task Progress
 █ Start-only
 █ Duration-only
 █ Baseline Split
 █ Milestone
 █ Summary
 █ Project Summary
 █ External Milestone
 █ Inactive Milestone
 █ Deadline

ID	Task Name	Duration	Start	Finish	October 2015	November 2015	December 2015	January 2016	February 2016	March 2016	April 2016	May 2016	Jun
					09/27 10/04 10/11 10/18 10/25	11/01 11/08 11/15 11/22 11/29 12/06 12/13 12/20 12/27	01/03 01/10 01/17 01/24	02/07 02/14 02/21 02/28	03/06 03/13 03/20 03/27	04/03 04/10 04/17 04/24	05/01 05/08 05/15 05/22 05/29		
62	Clearing and Grubbing for Road Construction	2 days	Wed 01/27/16	Thu 01/28/16					0%				
63	Demo East Logan Ave N Centerline	7 days	Fri 01/29/16	Mon 02/08/16					0%				
64	Roadway Reconstruction	18 days	Tue 02/09/16	Fri 03/04/16					0%				
65	Complete Stage 1 Roadway Excavation	8 days	Tue 02/09/16	Fri 02/19/16					0%				
66	Place Crushed Rock Base and Grade for HMA	8 days	Tue 02/09/16	Fri 02/19/16					0%				
67	Install Curb on the East Side Of Logan Ave	2 days	Mon 02/22/16	Tue 02/23/16									
68	Base Pave Logan Ave Stage 1	1 day	Wed 02/24/16	Wed 02/24/16									
69	Grade for Lightside Concrete	5 days	Wed 02/24/16	Tue 03/01/16					0%				
70	Cement Conc. Traffic Curb and Gutter	1 day	Thu 02/25/16	Thu 02/25/16									
71	Cement Conc. Traffic Curb	1 day	Fri 02/26/16	Fri 02/26/16									
72	Cement Conc. Pedestrian Curb	1 day	Mon 02/29/16	Mon 02/29/16									
73	Cement Concrete Driveway Entrance	1 day	Tue 03/01/16	Tue 03/01/16									
74	Decorative Cement Concrete Sidewalk	1 day	Wed 03/02/16	Wed 03/02/16									
75	Cement Conc Curb Ramp Type B	1 day	Thu 03/03/16	Thu 03/03/16									
76	Property Restoration	1 day	Fri 03/04/16	Fri 03/04/16									
77	Phase 2 (West Logan)	33 days	Fri 03/04/16	Tue 04/19/16					0%				
78	Traffic Control	2 days	Fri 03/04/16	Mon 03/07/16					0%				
79	Install Traffic Detour Phase 2	1 day	Fri 03/04/16	Fri 03/04/16									
80	Temporary Pavement Marking	1 day	Mon 03/07/16	Mon 03/07/16									
81	Demolition	8 days	Tue 03/08/16	Thu 03/17/16					0%				
82	Clearing and Grubbing	1 day	Tue 03/08/16	Tue 03/08/16									
83	Demo West Logan Ave N Centerline	7 days	Wed 03/09/16	Thu 03/17/16					0%				
84	Storm System	0.5 days	Fri 03/18/16	Fri 03/18/16									
85	Install DR2	0.5 days	Fri 03/18/16	Fri 03/18/16									
86	Electrical	2 days	Fri 03/18/16	Mon 03/21/16					0%				
87	Install Illumination Conduit	2 days	Fri 03/18/16	Mon 03/21/16					0%				
88	Roadway Reconstruction	19 days	Fri 03/18/16	Wed 04/13/16					0%				
89	Complete Stage 2 Roadway Excavation	7 days	Fri 03/18/16	Mon 03/28/16					0%				
90	Place Crushed Rock Base and Grade for HMA	7 days	Fri 03/18/16	Mon 03/28/16					0%				
91	Install Roadway Curb	3 days	Tue 03/29/16	Thu 03/31/16									

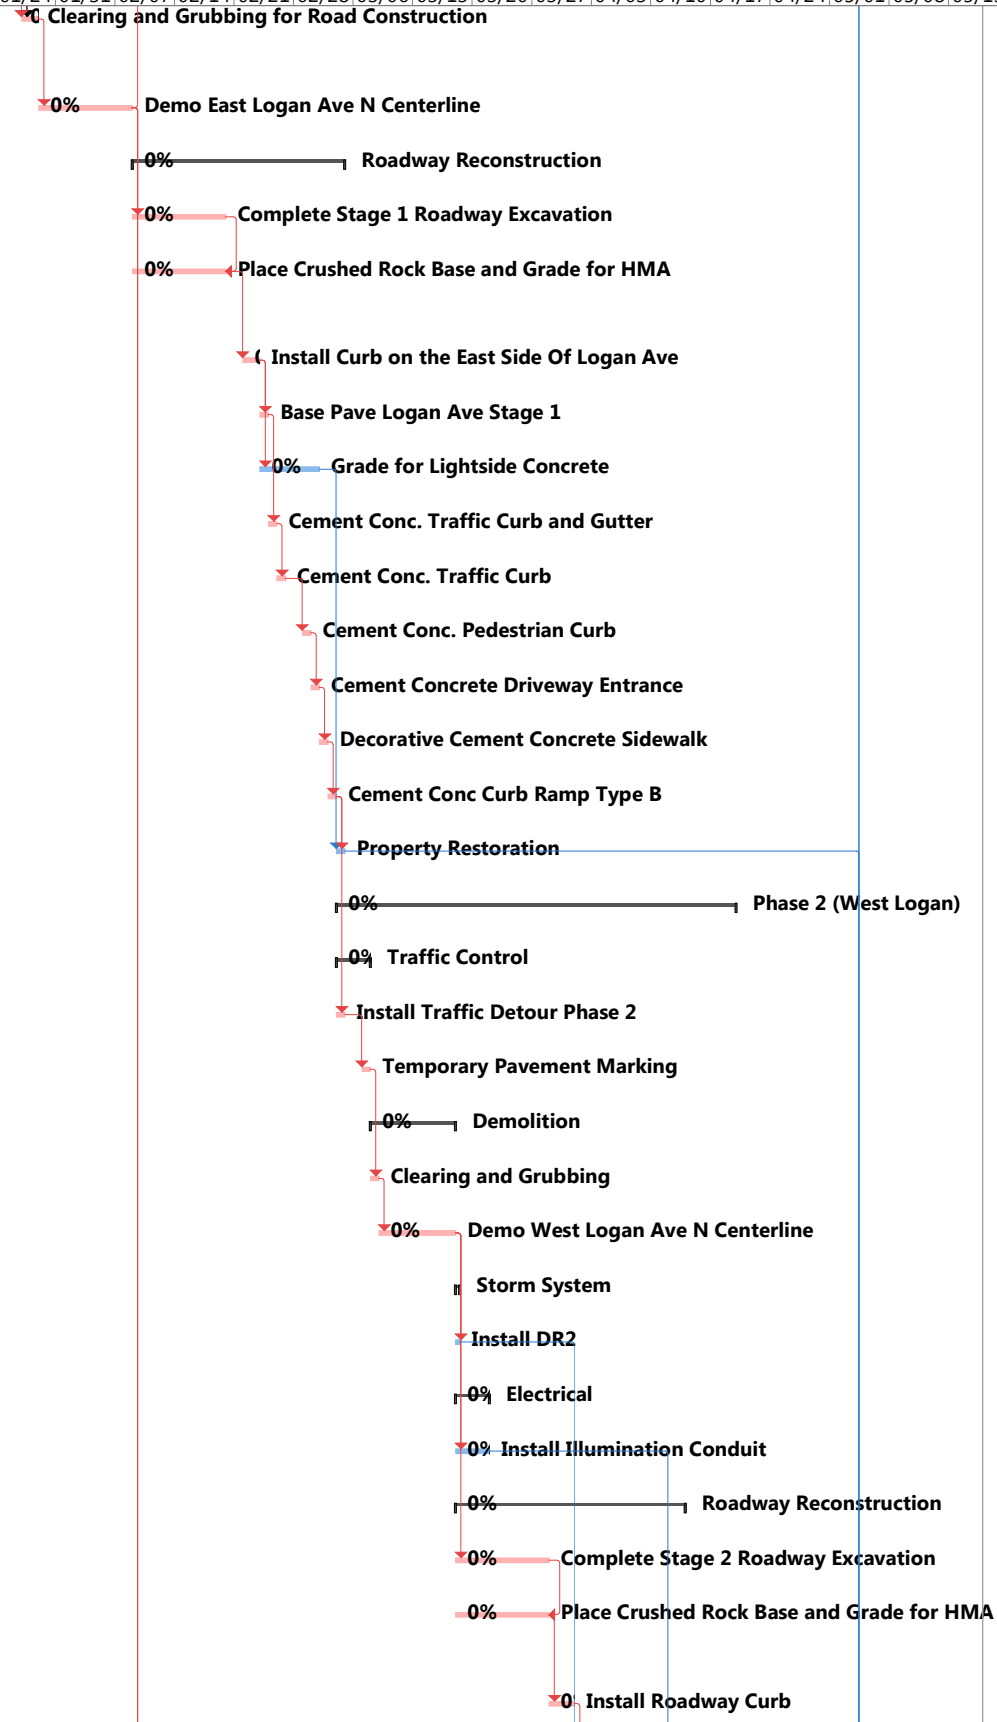

Contact No. TA 4951

█ Critical Progress █ Split █ Manual Task █ Finish-only █ Baseline █ Baseline Milestone █ Summary Progress █ Manual Summary █ External Tasks █ Inactive Task █ Inactive Summary
█ Critical Split █ Task █ Task Progress █ Start-only █ Duration-only █ Baseline Split █ Milestone █ Summary █ Project Summary █ External Milestone █ Inactive Milestone █ Deadline

