3rd/4th Corridor Improvements-Phase 1 Intersection Improvements

Date: Mon 8/27/12

ID	Task Name	Duration	Start	Finish
1	**Project Summary**	**120 days**	**Thu 8/23/12**	**Thu 3/28/13**
2	Mobilization	4 days	Thu 8/23/12	Tue 8/28/12
3	Security Fence	2 days	Thu 8/23/12	Fri 8/24/12
4	Surveying	3 days	Wed 8/29/12	Fri 8/31/12
5	**Whitman Ct**	**9 days**	**Tue 9/4/12**	**Fri 9/14/12**
6	Clear & Grub	2 days	Tue 9/4/12	Wed 9/5/12
7	Storm System	3 days	Thu 9/6/12	Mon 9/10/12
8	Earth Wall	2 days	Tue 9/11/12	Wed 9/12/12
9	Bioswale	2 days	Thu 9/13/12	Fri 9/14/12
10	**4th St-North**	**78 days**	**Mon 9/17/12**	**Wed 2/20/13**
11	Channelization	2 days	Mon 9/17/12	Tue 9/18/12
12	Silt /Security Fence	1 day	Wed 9/19/12	Wed 9/19/12
13	Clear & Grub	2 days	Thu 9/20/12	Fri 9/21/12
14	Sidewalk Removal	2 days	Mon 9/24/12	Tue 9/25/12
15	Joint Utility Trench	14 days	Wed 9/26/12	Mon 10/15/12
16	Remove Curb & Gutter	2 days	Tue 10/16/12	Wed 10/17/12
17	Demo Exist Storm System	2 days	Thu 10/18/12	Fri 10/19/12
18	Water Line (8")	3 days	Mon 10/22/12	Wed 10/24/12
19	Storm System	10 days	Thu 10/25/12	Wed 11/7/12
20	Remove ACP	2 days	Thu 11/8/12	Fri 11/9/12
21	Road Paving	6 days	Mon 11/12/12	Thu 1/3/13
22	Earth Wall	4 days	Fri 1/4/13	Wed 1/9/13
23	Water Line (12" & 16")	14 days	Thu 1/10/13	Wed 1/30/13
24	Curb & Gutter	3 days	Thu 1/31/13	Mon 2/4/13
25	Sidewalk	4 days	Tue 2/5/13	Fri 2/8/13
26	ACP	5 days	Mon 2/11/13	Fri 2/15/13
27	Channelization	2 days	Tue 2/19/13	Wed 2/20/13
28	Irrigation System	5 days	Thu 1/3/13	Wed 1/9/13
29	Topsoil/Planting/Bark	6 days	Thu 1/10/13	Thu 1/17/13
30	**4th St-South**	**26 days**	**Thu 2/21/13**	**Thu 3/28/13**
31	Demo	3 days	Thu 2/21/13	Mon 2/25/13
32	Curb,Gutter,Sidewalk (USPS)	4 days	Tue 2/26/13	Fri 3/1/13
33	ACP	3 days	Mon 3/4/13	Wed 3/6/13
34	Storm System	3 days	Thu 3/7/13	Mon 3/11/13
35	Demo Roadway	2 days	Tue 3/12/13	Wed 3/13/13
36	Roadway Paving	4 days	Thu 3/14/13	Tue 3/19/13
37	Curb,Gutter,Sidewalk	2 days	Wed 3/20/13	Thu 3/21/13
38	Permanent Channelization	3 days	Fri 3/22/13	Tue 3/26/13
39	Deco Conc Paving	2 days	Wed 3/27/13	Thu 3/28/13
40	Irrigation System	5 days	Thu 2/21/13	Wed 2/27/13
41	Topsoil/Planting/Bark	6 days	Thu 2/28/13	Thu 3/7/13
42	No Work at Safeway & AutoZone		Sat 11/17/12	Wed 1/2/13

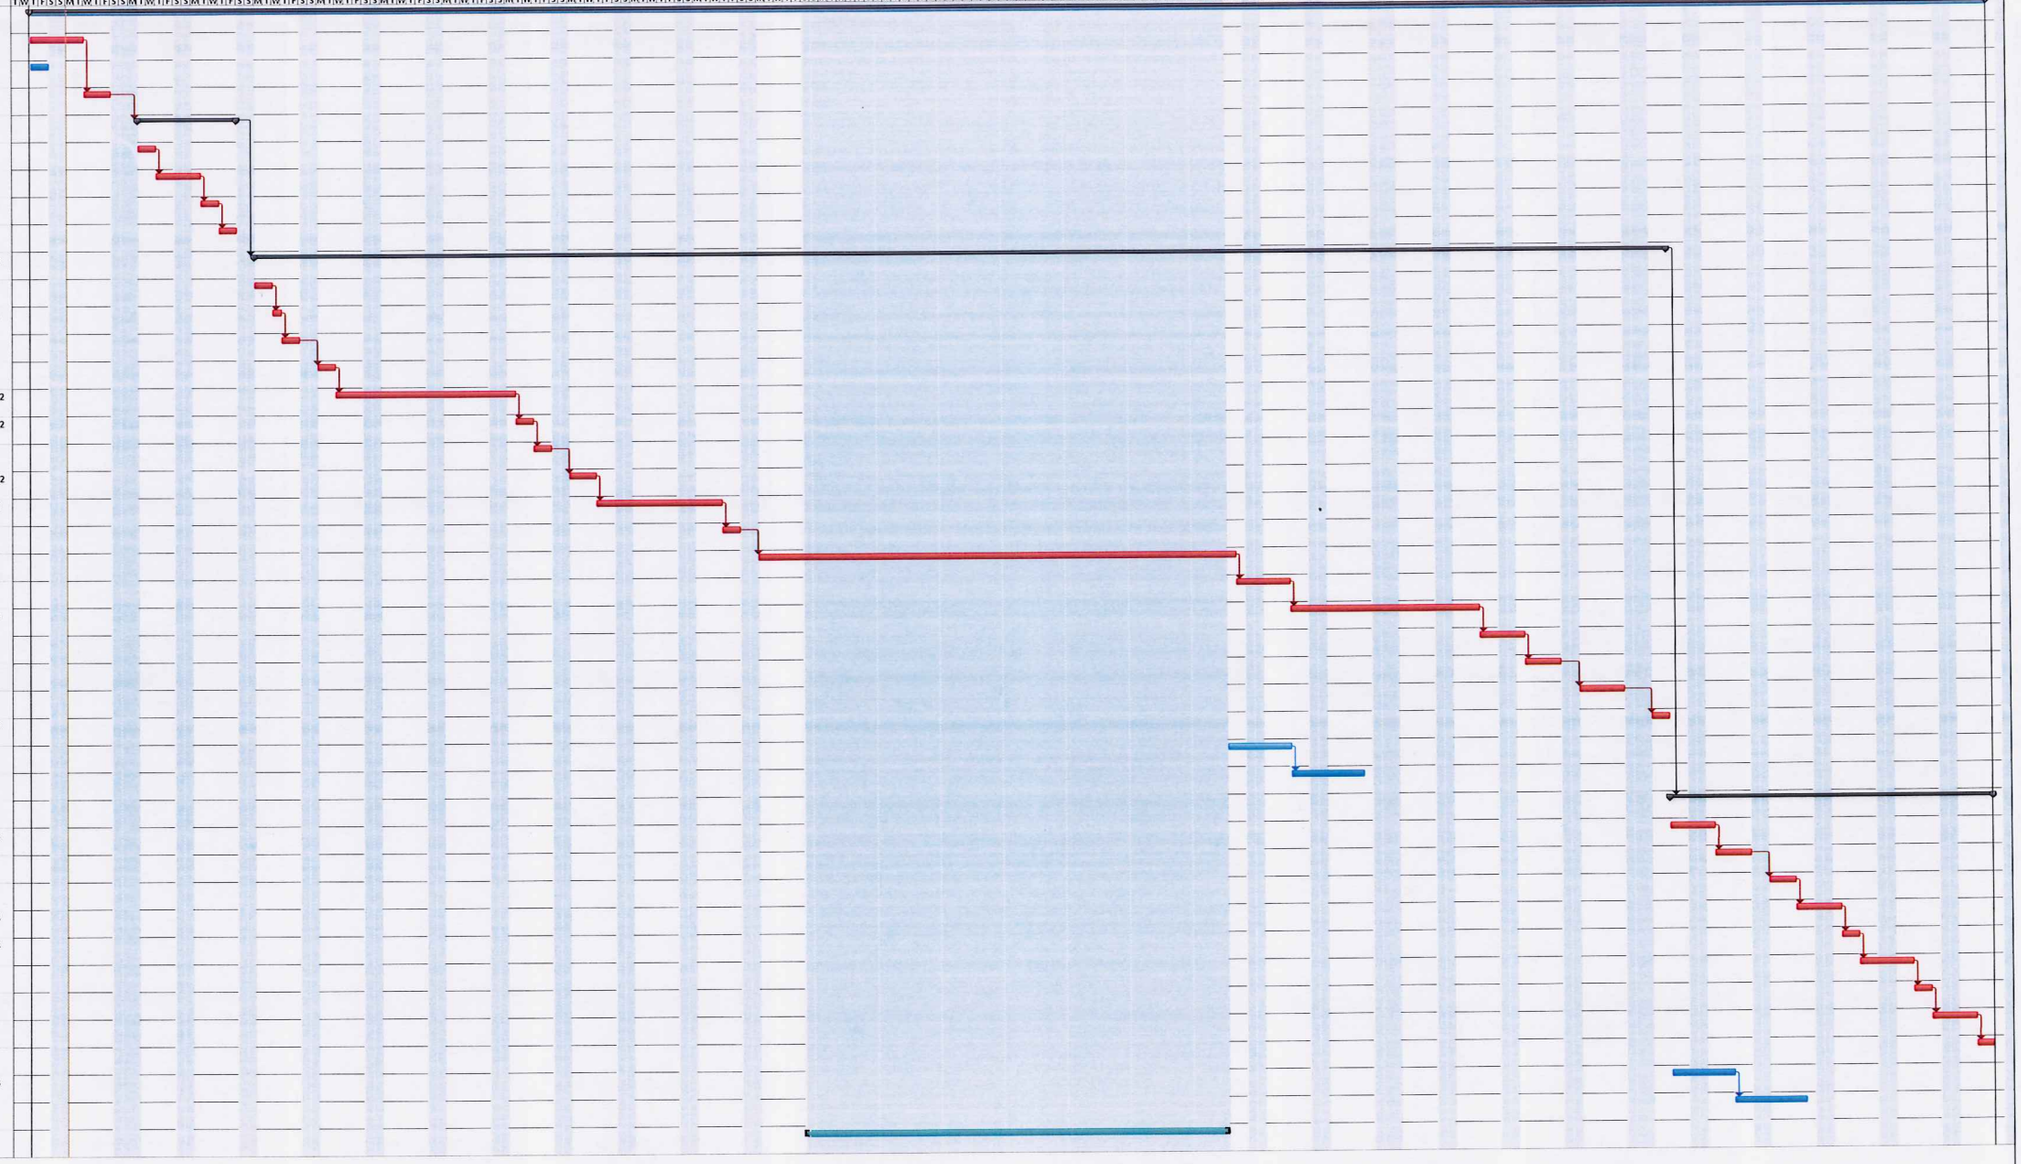

Owner: City of Renton
Contractor: Sanders General Construction

Actual Start Date: Thu 8/23/12
Scheduled Finish Date: Thu 3/28/13
