ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
0	**Rainier Ave Phase 4 Project Schedule**	**740 d?**	**0 d?**	**0 d?**	**Wed 11/2/22**	**NA**	**Wed 11/2/22**	**Mon 11/10/25**	**Wed 11/2/22**	**Mon 11/10/25**		
1												
2	Bid Opening Date	1 d	0 d	0 d	Wed 11/2/22	Wed 11/2/22	Wed 11/2/22	Wed 11/2/22	Wed 11/2/22	Wed 11/2/22		Project Overview
3	Award Date (w/in 45 calendar days after opening bids)	1.13 d	0 d	0 d	Tue 12/13/22	Tue 12/13/22	Tue 12/13/22	Tue 12/13/22	Tue 12/13/22	Tue 12/13/22	2FS+45 d	Project Overview
4	Contract Execution Date	1 d	0 d	0 d	Thu 12/22/22	Thu 12/22/22	Thu 12/22/22	Thu 12/22/22	Thu 12/22/22	Thu 12/22/22	3	Project Overview
5	Notice to Proceed Date	1 d	0 d	0 d	Mon 3/13/23	Mon 3/13/23	Mon 3/13/23	Mon 3/13/23	Mon 3/13/23	Mon 3/13/23	3,20FS+8 d	Project Overview
6	Substantial Completion Date	0 d	0 d	0 d	NA	NA	Mon 11/10/25	Mon 11/10/25	Mon 11/10/25	Mon 11/10/25	536,540,324,354,472,288,471,539	Project Overview
7	Physical Completion Date	0 d	0 d	0 d	NA	NA	Mon 11/10/25	Mon 11/10/25	Mon 11/10/25	Mon 11/10/25	5,6	Project Overview
8	Contractual Physical Completion Date (500 working days)	0 d	154 d	154 d	NA	NA	Wed 4/2/25	Wed 4/2/25	Mon 11/10/25	Mon 11/10/25	5FS+500 d	Project Overview
9												
10	**Preconstruction**	**164 d**	**0 d**	**0 d**	**Sun 2/12/23**	**Fri 10/6/23**	**Sun 2/12/23**	**Fri 10/6/23**	**Sun 2/12/23**	**Fri 10/6/23**	**4**	
11	Submit Contractor's Health and Safety Plan	0 d	0 d	0 d	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	4	Pivetta - Administration
12	Prepare/Submit Confined Space Entry Program	5 d	0 d	0 d	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	5	Pivetta - Administration
13	Prepare/Submit Shoring and Excavation Plan	3 d	0 d	0 d	Wed 2/15/23	Fri 2/17/23	Wed 2/15/23	Fri 2/17/23	Wed 2/15/23	Fri 2/17/23	4	Pivetta - Administration
14	Prepare/Submit Breakdown of Lump Sum Bid Items	5 d	0 d	0 d	Sun 2/12/23	Fri 2/17/23	Sun 2/12/23	Fri 2/17/23	Sun 2/12/23	Fri 2/17/23	4	Pivetta - Administration
15	Prepare/Submit Preliminary QPL/RAM for Jobsite Materials	5 d	0 d	0 d	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	4	Pivetta - Administration
16	Prepare/Submit Preliminary Schedule of Working Drawing Submittals	5 d	0 d	0 d	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	4	Pivetta - Administration
17	Submit Work Hour Variance to CoR	0 d	0 d	0 d	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	4	Pivetta - Administration
18	Prepare/Submit Type 2 Working Drawings for Field Office	1 d	0 d	0 d	Thu 3/2/23	Thu 3/2/23	Thu 3/2/23	Thu 3/2/23	Thu 3/2/23	Thu 3/2/23	4	Pivetta - Administration
19	Submit Preliminary Type B Schedule	1 d	0 d	0 d	Tue 2/21/23	Tue 2/21/23	Tue 2/21/23	Tue 2/21/23	Tue 2/21/23	Tue 2/21/23	4	Pivetta - Administration
20	Attend Preconstruction Conference	1 d	0 d	0 d	Wed 2/22/23	Wed 2/22/23	Wed 2/22/23	Wed 2/22/23	Wed 2/22/23	Wed 2/22/23	4FS+49 d,11,14,15,16,17,18,19	City of Renton
21												
22	Submit Final Type B Progress Schedule	1 d	0 d	0 d	Mon 3/20/23	Mon 3/20/23	Mon 3/20/23	Mon 3/20/23	Mon 3/20/23	Mon 3/20/23	20	Pivetta - Administration
23	Prepare/Submit Project Specific Traffic Control Plan	0 d	0 d	0 d	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	4	Pivetta - Administration
24	Prepare/Submit Confined Space Program Plan	5 d	0 d	0 d	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23		Pivetta - Administration
25	Submit/Fabricate Sample Project Identification Signs to CoR	5 d	0 d	0 d	Mon 2/20/23	Mon 2/27/23	Mon 2/20/23	Mon 2/27/23	Mon 2/20/23	Mon 2/27/23	4	Pivetta - Administration
26	Prepare/Submit Dewatering Plan (Waiting on RFI-007 submitted 2/20/2023)	5 d	0 d	0 d	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	Mon 10/2/23	Fri 10/6/23	4	Pivetta - Administration
27	Prepare/Submit Contaminated Soil and GW Handling and Mgmt Plan	0 d	0 d	0 d	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	4	Pivetta - Administration
28	Request JUT Structures and Conduit	1 d	0 d	0 d	Wed 3/8/23	Wed 3/8/23	Wed 3/8/23	Wed 3/8/23	Wed 3/8/23	Wed 3/8/23	20	Pivetta - Administration
29	Utility Preconstruction Meeting	1 d	0 d	0 d	Thu 3/16/23	Thu 3/16/23	Thu 3/16/23	Thu 3/16/23	Thu 3/16/23	Thu 3/16/23	5FS+2 d	City of Renton
30												
31	Setup/Install Temporary Field Offices	0 d	0 d	0 d	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	20	Pivetta
32	Complete Project Existing Conditions Survey	4 d	0 d	0 d	Mon 3/13/23	Fri 3/17/23	Mon 3/13/23	Fri 3/17/23	Mon 3/13/23	Fri 3/17/23	5	Pivetta - Administration
33	Control and Staking	0 d	0 d	0 d	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	Mon 2/20/23	5	North Peak
34												
35	**Rainier Ave. S. - Construction Duration**	**655 d?**	**0 d?**	**0 d?**	**Mon 3/13/23**	**NA**	**Mon 3/13/23**	**Mon 11/10/25**	**Mon 3/13/23**	**Mon 11/10/25**	**5,13**	
36	**Mobilization**	**107 d**	**0 d**	**0 d**	**Mon 3/13/23**	**Fri 8/11/23**	**Mon 3/13/23**	**Fri 8/11/23**	**Mon 3/13/23**	**Fri 8/11/23**		
37	CCTV and Flush Sewer Lines	0 d	0 d	0 d	Tue 8/1/23	Tue 8/1/23	Tue 8/1/23	Tue 8/1/23	Tue 8/1/23	Tue 8/1/23	5,12	Insituform
38	Fence Removal and Reinstallation	5 d	0 d	0 d	Tue 8/1/23	Mon 8/7/23	Tue 8/1/23	Mon 8/7/23	Tue 8/1/23	Mon 8/7/23	33SS	Pivetta
39	Sewer Manhole Delivery	39 d	0 d	0 d	Fri 6/16/23	Fri 8/11/23	Fri 6/16/23	Fri 8/11/23	Fri 6/16/23	Fri 8/11/23	5	Pivetta - Administration
40												
41	**Potholing**	**42 d**	**0 d**	**0 d**	**Mon 3/13/23**	**Tue 5/9/23**	**Mon 3/13/23**	**Tue 5/9/23**	**Mon 3/13/23**	**Tue 5/9/23**		
42	Pothole South Rainer Ave - STA 15+25 to 25+00	17 d	0 d	0 d	Mon 3/13/23	Wed 4/5/23	Mon 3/13/23	Wed 4/5/23	Mon 3/13/23	Wed 4/5/23	5,23	
43	Pothole North Rainier Ave - STA 25+00 to 42+85	24 d	0 d	0 d	Wed 4/5/23	Tue 5/9/23	Wed 4/5/23	Tue 5/9/23	Wed 4/5/23	Tue 5/9/23	42	
44	Pothole Side Streets	0 d	0 d	0 d	Thu 5/4/23	Thu 5/4/23	Thu 5/4/23	Thu 5/4/23	Thu 5/4/23	Thu 5/4/23	43	
45												
46	**Stage 1 (West)**	**461 d?**	**183 d?**	**183 d?**	**Tue 3/28/23**	**NA**	**Tue 3/28/23**	**Thu 2/20/25**	**Tue 3/28/23**	**Mon 11/10/25**	**5**	
47	**Site Prep - Sta 13+93.10 to 40+80.29**	**133.25 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Fri 10/6/23**	**Tue 3/28/23**	**Fri 10/6/23**	**Tue 3/28/23**	**Fri 10/6/23**		
48	Install Project Identification and Business Owner Signs	1 d	0 d	0 d	Tue 3/28/23	Tue 3/28/23	Tue 3/28/23	Tue 3/28/23	Tue 3/28/23	Tue 3/28/23	4	Pivetta
49	Install High Visibility Fence/Inspection by CoR	1 d	0 d	0 d	Wed 3/29/23	Wed 3/29/23	Wed 3/29/23	Wed 3/29/23	Wed 3/29/23	Wed 3/29/23	4	Pivetta
50	Install TESC- Stage 1	28 d	0 d	0 d	Wed 3/29/23	Fri 5/5/23	Wed 3/29/23	Fri 5/5/23	Wed 3/29/23	Fri 5/5/23	4	Pivetta
51	Clear & Grub - Stage 1 (Work Progressing as Needed with Other Activities)	2.25 d	0 d	0 d	Mon 4/24/23	Wed 6/21/23	Mon 4/24/23	Wed 6/21/23	Mon 4/24/23	Wed 6/21/23	50	Pivetta
52	Complete Removals	5 d	0 d	0 d	Mon 4/24/23	Fri 10/6/23	Mon 4/24/23	Fri 10/6/23	Mon 4/24/23	Fri 10/6/23	51	Pivetta
53	Relocate Bus Shelter - Sta 27+45.48	3 d	0 d	0 d	Mon 4/24/23	Wed 4/26/23	Mon 4/24/23	Wed 4/26/23	Mon 4/24/23	Wed 4/26/23	5	Pivetta
54	**Temporary Channelization and Signalization - Sta 13+95 to 43+63.00**	**14 d**	**0 d**	**0 d**	**Wed 4/5/23**	**Mon 4/24/23**	**Wed 4/5/23**	**Mon 4/24/23**	**Wed 4/5/23**	**Mon 4/24/23**		
55	**Portable Temporary Signal System (SW Sunset/S 3rd St.) (2nd St.) (Airport Way/Renton Ave)**	**6 d**	**0 d**	**0 d**	**Wed 4/5/23**	**Wed 4/12/23**	**Wed 4/5/23**	**Wed 4/12/23**	**Wed 4/5/23**	**Wed 4/12/23**		
56	Pull Wire to Tie In Temp Signal	2 d	0 d	0 d	Wed 4/5/23	Thu 4/6/23	Wed 4/5/23	Thu 4/6/23	Wed 4/5/23	Thu 4/6/23	48	Golden Gate
57	Video Detection Camera Installation	1 d	0 d	0 d	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	56SS+2 d	Golden Gate
58	Install Portable Signal System	1 d	0 d	0 d	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	57	Golden Gate
59	Adjust and Modify Signals	1 d	0 d	0 d	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	58	Golden Gate
60	**Temporary Channelization - Sta 13+95 to 43+63.00**	**9 d**	**0 d**	**0 d**	**Wed 4/12/23**	**Mon 4/24/23**	**Wed 4/12/23**	**Mon 4/24/23**	**Wed 4/12/23**	**Mon 4/24/23**		

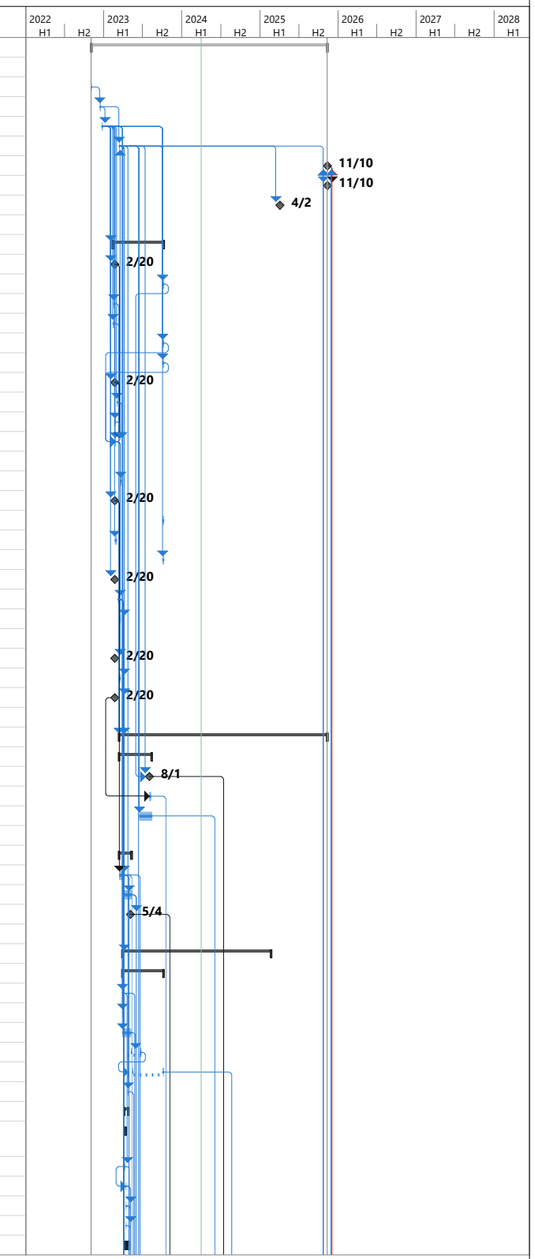

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
61	Install Stage 1 Construction Channelization and Striping - South of Airport Way	0 d	0 d	0 d	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	Wed 4/12/23	57,59,58,56,53,48FF	SPM
62	Install Stage 1 Construction Channelization and Striping - North of Airport Way	1 d	0 d	0 d	Mon 4/24/23	Mon 4/24/23	Mon 4/24/23	Mon 4/24/23	Mon 4/24/23	Mon 4/24/23	61	SPM
63	**Joint Utility Trench - Sta 15+25 to 42+85**	**242 d?**	**0 d?**	**0 d?**	**Tue 3/28/23**	**Fri 3/29/24**	**Tue 3/28/23**	**Fri 3/29/24**	**Tue 3/28/23**	**Fri 3/29/24**		
64	**JUT - Walgreens to Sansonia (Sections A, EE, AA) - Sta 15+25 to Sta 18+40**	**87 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Mon 7/31/23**	**Tue 3/28/23**	**Mon 7/31/23**	**Tue 3/28/23**	**Mon 7/31/23**		
65	Receive Vaults and Conduits from Utilities	10 d	0 d	0 d	Tue 3/28/23	Mon 6/5/23	Tue 3/28/23	Mon 6/5/23	Tue 3/28/23	Mon 6/5/23	5,28	Utilities
66	Install Vaults	3.5 d	0 d	0 d	Thu 5/11/23	Wed 6/7/23	Thu 5/11/23	Wed 6/7/23	Thu 5/11/23	Wed 6/7/23	65,74,42	Pivetta - JUT
67	Install Conduits	34 d	0 d	0 d	Mon 6/12/23	Mon 7/31/23	Mon 6/12/23	Mon 7/31/23	Mon 6/12/23	Mon 7/31/23	66	Pivetta - JUT/Golden Gate/PSE - Ga
68	**JUT - Night/Stage 2 - Hertz/Lyft to Taco Time - Sta 14+21.6 to 18+40**	**104 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Wed 8/23/23**	**Tue 3/28/23**	**Wed 8/23/23**	**Tue 3/28/23**	**Wed 8/23/23**		
69	Receive Vaults and Conduits from Utilities	6 d	0 d	0 d	Tue 3/28/23	Tue 5/30/23	Tue 3/28/23	Tue 5/30/23	Tue 3/28/23	Tue 5/30/23	28	Utilities
70	Install Vaults	2 d	0 d	0 d	Mon 7/31/23	Tue 8/1/23	Mon 7/31/23	Tue 8/1/23	Mon 7/31/23	Tue 8/1/23	69	
71	Install Conduits	8 d	0 d	0 d	Mon 8/14/23	Wed 8/23/23	Mon 8/14/23	Wed 8/23/23	Mon 8/14/23	Wed 8/23/23	75,70	Pivetta - JUT/Golden Gate/PSE - Ga
72	**JUT - Night/Crossing - Watson Sec to Taco Time, Across 2nd St., Vacant to Metro PCS - Sta 18+40 to 20+10**	**108 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Tue 8/29/23**	**Tue 3/28/23**	**Tue 8/29/23**	**Tue 3/28/23**	**Tue 8/29/23**		
73	Receive Vaults and Conduits from Utilities	10 d	0 d	0 d	Tue 3/28/23	Mon 6/5/23	Tue 3/28/23	Mon 6/5/23	Tue 3/28/23	Mon 6/5/23	28	Utilities
74	Install Vaults	12 d	0 d	0 d	Tue 6/20/23	Fri 7/7/23	Tue 6/20/23	Fri 7/7/23	Tue 6/20/23	Fri 7/7/23	73,42	Pivetta - JUT
75	Install Conduits	21 d	0 d	0 d	Tue 8/1/23	Tue 8/29/23	Tue 8/1/23	Tue 8/29/23	Tue 8/1/23	Tue 8/29/23	73,74,67	Pivetta - JUT/Golden Gate/PSE - Ga
76	**JUT - Night/Stage 2 - Vacant to Formula 1 Fast Lube - Sta 20+10 to 25+20**	**114 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Thu 9/7/23**	**Tue 3/28/23**	**Thu 9/7/23**	**Tue 3/28/23**	**Thu 9/7/23**		
77	Remove/Relocate Bus Shelter - Sta 24+59.90	4 d	0 d	0 d	Mon 6/12/23	Thu 6/15/23	Mon 6/12/23	Thu 6/15/23	Mon 6/12/23	Thu 6/15/23	5	Pivetta - JUT
78	Receive Vaults and Conduits from Utilities	1 d	0 d	0 d	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	28	Utilities
79	Install Vaults	4 d	0 d	0 d	Wed 8/30/23	Tue 9/5/23	Wed 8/30/23	Tue 9/5/23	Wed 8/30/23	Tue 9/5/23	78,77,70	
80	Install Conduits	6 d	0 d	0 d	Wed 8/30/23	Thu 9/7/23	Wed 8/30/23	Thu 9/7/23	Wed 8/30/23	Thu 9/7/23	79	Pivetta - JUT/Golden Gate/PSE - Ga
81	**JUT - Big Island Poke to Watson Security (Sections B, C, F, D, R, K, M, JJ, DD, LL, E, G, H, Z) - Sta 19+00 to 24+80**	**153 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Fri 11/3/23**	**Tue 3/28/23**	**Fri 11/3/23**	**Tue 3/28/23**	**Fri 11/3/23**		
82	Receive Vaults and Conduits from Utilities	1 d	0 d	0 d	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	28	Utilities
83	Install Vaults (J07 Installed Last with RFI-072)	0 d	0 d	0 d	Mon 5/15/23	Mon 7/17/23	Mon 5/15/23	Mon 7/17/23	Mon 5/15/23	Mon 7/17/23	82,65,79	Pivetta - JUT
84	**Install Conduits**	**38 d**	**0 d**	**0 d**	**Mon 9/11/23**	**Fri 11/3/23**	**Mon 9/11/23**	**Fri 11/3/23**	**Mon 9/11/23**	**Fri 11/3/23**		
85	Install Conduits	23 d	0 d	0 d	Mon 9/11/23	Fri 11/3/23	Mon 9/11/23	Fri 11/3/23	Mon 9/11/23	Fri 11/3/23	82,83,298,67,71,80	Pivetta - JUT/Golden Gate/PSE - Ga
86	Contaminated Soils at STA 21+50	9 d	0 d	0 d	Thu 9/28/23	Tue 10/10/23	Thu 9/28/23	Tue 10/10/23	Thu 9/28/23	Tue 10/10/23	85SS	
87	**JUT - Night/Power Crossting - Sta 23+80**	**3 d**	**0 d**	**0 d**	**Mon 10/2/23**	**Wed 10/4/23**	**Mon 10/2/23**	**Wed 10/4/23**	**Mon 10/2/23**	**Wed 10/4/23**		
88	Install Conduits (Deleted Per FD)	3 d	0 d	0 d	Mon 10/2/23	Wed 10/4/23	Mon 10/2/23	Wed 10/4/23	Mon 10/2/23	Wed 10/4/23		Pivetta - JUT/Golden Gate/PSE - Ga
89	**JUT - Victoria Street (CO-09)**	**8 d**	**0 d**	**0 d**	**Mon 11/20/23**	**Fri 12/1/23**	**Mon 11/20/23**	**Fri 12/1/23**	**Mon 11/20/23**	**Fri 12/1/23**		
90	Install Conduits	8 d	0 d	0 d	Mon 11/20/23	Fri 12/1/23	Mon 11/20/23	Fri 12/1/23	Mon 11/20/23	Fri 12/1/23	95	
91	**JUT - Watson Security to Renton Ave. Ext (NO PSE Gas) - Sta 24+80 to 31+90**	**186 d?**	**0 d?**	**0 d?**	**Tue 3/28/23**	**Fri 1/5/24**	**Tue 3/28/23**	**Fri 1/5/24**	**Tue 3/28/23**	**Fri 1/5/24**		
92	Receive Vaults and Conduits from Utilities	1 d	0 d	0 d	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	28	Utilities
93	Install Vaults	12 d	0 d	0 d	Tue 5/23/23	Tue 10/17/23	Tue 5/23/23	Tue 10/17/23	Tue 5/23/23	Tue 10/17/23	92,83,43	Pivetta - JUT
94	**Install Conduits**	**9 d?**	**0 d?**	**0 d?**	**Mon 11/6/23**	**Fri 1/5/24**	**Mon 11/6/23**	**Fri 11/17/23**	**Mon 11/6/23**	**Fri 1/5/24**	**93**	**Pivetta - JUT/Golden Gate/PSE - Ga**
95	Watson Security to Hayes	4 d	0 d	0 d	Mon 11/6/23	Fri 11/17/23	Mon 11/6/23	Fri 11/17/23	Mon 11/6/23	Fri 11/17/23	85	
96	Hayes to Renton Ave	4 d	0 d	0 d	Mon 12/4/23	Fri 1/5/24	Mon 12/4/23	Fri 1/5/24	Mon 12/4/23	Fri 1/5/24	95,90	
97	Contaminated Soil @ STA 28+75	2 d	0 d	0 d	Tue 12/12/23	Wed 12/13/23	Tue 12/12/23	Wed 12/13/23	Tue 12/12/23	Wed 12/13/23	96SS	
98	**JUT - Night/Power Crossing - Tobin St, Sta 28+75 and 30+28**	**4 d**	**0 d**	**0 d**	**Wed 1/24/24**	**Mon 1/29/24**	**Wed 1/24/24**	**Mon 1/29/24**	**Wed 1/24/24**	**Mon 1/29/24**		
99	Install Conduits	4 d	0 d	0 d	Wed 1/24/24	Mon 1/29/24	Wed 1/24/24	Mon 1/29/24	Wed 1/24/24	Mon 1/29/24	94,96,103	Pivetta - JUT/Golden Gate/PSE - Ga
100	**JUT - Night/Crossing Renton Ave Ext - Sta 31+90 to 33+00**	**194 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Tue 1/23/24**	**Tue 3/28/23**	**Tue 1/23/24**	**Tue 3/28/23**	**Tue 1/23/24**		
101	Receive Vaults and Conduits from Utilities	1 d	0 d	0 d	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	28	Utilities
102	Install Vaults	4 d	0 d	0 d	Mon 10/2/23	Thu 10/5/23	Mon 10/2/23	Thu 10/5/23	Mon 10/2/23	Thu 10/5/23	101,62	Pivetta - JUT
103	Install Conduits	7 d	0 d	0 d	Mon 1/8/24	Tue 1/23/24	Mon 1/8/24	Tue 1/23/24	Mon 1/8/24	Tue 1/23/24	101,102,96	Pivetta - JUT/Golden Gate/PSE - Ga
104	**JUT - Arco to Gerber Collision- Section P, U, V, W (No PSE Gas) - Sta 33+00 to 42+85**	**242 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Fri 3/29/24**	**Tue 3/28/23**	**Fri 3/29/24**	**Tue 3/28/23**	**Fri 3/29/24**		
105	Receive Vaults and Conduits from Utilities	1 d	0 d	0 d	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	28	Utilities
106	Install Vaults	17 d	0 d	0 d	Wed 10/18/23	Fri 1/5/24	Wed 10/18/23	Fri 1/5/24	Wed 10/18/23	Fri 1/5/24	93,105,38	Pivetta - JUT
107	Install Conduits	25 d	0 d	0 d	Wed 2/14/24	Fri 3/29/24	Wed 2/14/24	Fri 3/29/24	Wed 2/14/24	Fri 3/29/24	105,106,111	Pivetta - JUT/Golden Gate/PSE - Ga
108	**JUT - Night/Crossings - Sta 33+77, 36+17, 40+43**	**206 d**	**0 d**	**0 d**	**Tue 3/28/23**	**Thu 2/8/24**	**Tue 3/28/23**	**Thu 2/8/24**	**Tue 3/28/23**	**Thu 2/8/24**		
109	Receive Vaults and Conduits from Utility Owner	1 d	0 d	0 d	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	Tue 3/28/23	Wed 6/21/23	28	Utilities
110	Install Vaults	1 d	0 d	0 d	Wed 10/18/23	Wed 10/18/23	Wed 10/18/23	Wed 10/18/23	Wed 10/18/23	Wed 10/18/23	106SS,102,109	Pivetta - JUT
111	Install Conduit	8 d	0 d	0 d	Tue 1/30/24	Thu 2/8/24	Tue 1/30/24	Thu 2/8/24	Tue 1/30/24	Thu 2/8/24	110,99	Pivetta - JUT/Golden Gate/PSE - Ga
112	**JUT - Utility Owner Work, Removals, Grounding/Bonding 15+25 to 42+85**	**197 d**	**32 d**	**32 d**	**Mon 10/2/23**	**NA**	**Mon 10/2/23**	**Tue 7/30/24**	**Mon 10/2/23**	**Fri 9/13/24**		
113	Lumen/CenturyLink to Begin Work South of Victoria Street	0 d	0 d	0 d	Tue 1/23/24	Tue 1/23/24	Tue 1/23/24	Tue 1/23/24	Tue 1/23/24	Tue 1/23/24	94	
114	PSE Gas - Install 1-6" Gas Line & Connections to Main JUT across Rainier (Ends at HH/II in SW Victoria)	28 d	0 d	0 d	Mon 10/2/23	Thu 1/4/24	Mon 10/2/23	Thu 1/4/24	Mon 10/2/23	Thu 1/4/24	67SS	PSE - Gas
115	Relocate Gas Line on Airport Way to Avoid Storm Drain	4 d	0 d	0 d	Mon 1/8/24	Thu 1/11/24	Mon 1/8/24	Thu 1/11/24	Mon 1/8/24	Thu 1/11/24		
116	Rem/Abandon Existing PSE Gas Main	60 d	81 d	81 d	Mon 10/2/23	NA	Mon 10/2/23	Fri 5/17/24	Mon 10/2/23	Fri 9/13/24	114SS	PSE - Gas
117	**PSE - Pull Wire (Power and Fiber) and Complete Connections**	**32 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 4/1/24**	**Tue 5/14/24**	**Mon 4/1/24**	**Mon 8/19/24**	**110,107**	**Utilities**
118	**CO-21 Golden Gate Complete Business Connections - Execute CO and Order Materials**	10 d	78 d	0 d	NA	NA	Mon 4/1/24	Fri 4/12/24	Tue 7/23/24	Mon 8/5/24	107	
119	**CO-21 Golden Gate Complete Business Connections - Install**	10 d	78 d	78 d	NA	NA	Mon 4/15/24	Fri 4/26/24	Tue 8/6/24	Mon 8/19/24	118	

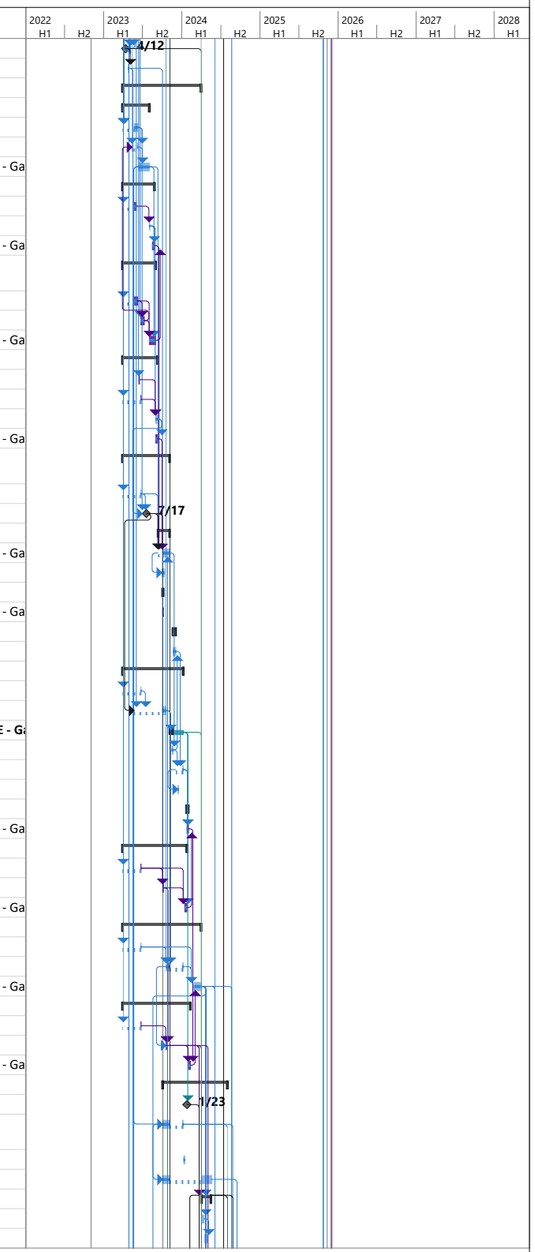

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
120	PSE - Install Transformers - V02A, V0X, V15A, V16A	30 d	30 d	30 d	NA	NA	Mon 4/1/24	Fri 5/10/24	Mon 5/13/24	Tue 6/25/24	107	PSE - Electric
121	Complete PSE Swap Overs	30 d	0 d	0 d	NA	NA	Mon 4/1/24	Fri 5/10/24	Mon 4/1/24	Fri 5/10/24	107	
122	PSE Pole Removal and Installation - S. Tobin St. - Sta 501+51.37 (moved from JUT to conversion)	2 d	66 d	66 d	NA	NA	Mon 5/13/24	Tue 5/14/24	Fri 8/16/24	Mon 8/19/24	121	PSE - Electric
123	**Lumen/Centurylink - Pull Wire and Complete Connections Project Wide**	**54 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 4/1/24**	**Fri 6/14/24**	**Mon 4/1/24**	**Mon 7/1/24**	**117SS,110,113,107**	**Centurylink**
124	Complete Lumen Connections Tobin South	30 d	0 d	0 d	NA	NA	Mon 4/1/24	Fri 5/10/24	Mon 4/1/24	Fri 5/10/24	107	
125	Complete Lumen Connections Tobin North	24 d	10 d	0 d	NA	NA	Mon 5/13/24	Fri 6/14/24	Tue 5/28/24	Mon 7/1/24	124	
126	Comcast - Pull Wire and Complete Connections	30 d	0 d	0 d	NA	NA	Mon 4/1/24	Fri 5/10/24	Mon 4/1/24	Fri 5/10/24	123SS,110,107	Comcast
127	**Remove Existing Vaults, Pedestals, and Risers**	**54 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 5/13/24**	**Tue 7/30/24**	**Mon 5/13/24**	**Tue 8/13/24**	**120SS,123SS,126SS**	**Utilities**
128	CO-24 Remove Existing JUT Tobin South	32 d	0 d	0 d	NA	NA	Mon 5/13/24	Thu 6/27/24	Mon 5/13/24	Thu 6/27/24	124,121,126	
129	CO-24 Remove Existing JUT Tobin North	30 d	10 d	10 d	NA	NA	Mon 6/17/24	Tue 7/30/24	Tue 7/2/24	Tue 8/13/24	125	
130	**5G Small Cell Network Conduit System - Sta 14+65 to 41+55**	**23 d**	**0 d**	**0 d**	**Mon 10/2/23**	**Wed 11/1/23**	**Mon 10/2/23**	**Wed 11/1/23**	**Mon 10/2/23**	**Wed 11/1/23**		
131	Trench and Conduit	21 d	0 d	0 d	Mon 10/2/23	Mon 10/30/23	Mon 10/2/23	Mon 10/30/23	Mon 10/2/23	Mon 10/30/23	67SS,107	Golden Gate
132	Boxes	2 d	0 d	0 d	Tue 10/31/23	Wed 11/1/23	Tue 10/31/23	Wed 11/1/23	Tue 10/31/23	Wed 11/1/23	131	Golden Gate
133	**Water Line/Night - Sta 14+02 to 42+14.5**	**459 d**	**183 d**	**183 d**	**Thu 3/30/23**	**NA**	**Thu 3/30/23**	**Thu 2/20/25**	**Thu 3/30/23**	**Mon 11/10/25**		
134	**Stage 1 Bypass, Cut and Cap**	**116 d**	**0 d**	**0 d**	**Mon 4/17/23**	**Mon 10/2/23**	**Mon 4/17/23**	**Mon 10/2/23**	**Mon 4/17/23**	**Mon 10/2/23**		
135	Cut and Cap Existing Waterline - Sta 15+55	4 d	0 d	0 d	Mon 4/17/23	Thu 4/20/23	Mon 4/17/23	Thu 4/20/23	Mon 4/17/23	Thu 4/20/23	42	Pivetta - Water/City of Renton Wat
136	Cut and Cap Existing Waterline - Taco Time to Buddy's Home Furnishings - Sta 18+20 to 21+00	0 d	0 d	0 d	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	135,42	Pivetta - Water/City of Renton Water
137	Cut and Cap Existing Waterline - SW Victoria - Sta 25+00 (Deleted - Work Not Required)	1 d	0 d	0 d	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23		Pivetta - Water/City of Renton Wat
138	Cut and Cap Waterline - S. Tobin St. - Sta 28+60 (Deleted - Work Not Required)	1 d	0 d	0 d	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23		Pivetta - Water/City of Renton Wat
139	**Water Line - Stage 1 - Sta 14+02.2 to 42+06.9 Rainier Ave, Sta 30+74.5 to 602+87.44 Airport Way**	**125 d**	**0 d**	**0 d**	**Tue 5/2/23**	**Mon 10/30/23**	**Tue 5/2/23**	**Mon 10/30/23**	**Tue 5/2/23**	**Mon 10/30/23**		
140	Install Water Line and Appurtenances	28 d	0 d	0 d	Tue 5/2/23	Mon 10/30/23	Tue 5/2/23	Mon 10/30/23	Tue 5/2/23	Mon 10/30/23	62,136	Pivetta - Water
141	FRPCS Concrete DMB (Deleted - Work Occurring with Water Line Install)	15 d	0 d	0 d	Mon 10/2/23	Fri 10/20/23	Mon 10/2/23	Fri 10/20/23	Mon 10/2/23	Fri 10/20/23		Pivetta - Water
142	Pressure Testing, Polypig, Disinfect Water Line	88 d	0 d	0 d	Wed 6/21/23	Tue 10/24/23	Wed 6/21/23	Tue 10/24/23	Wed 6/21/23	Tue 10/24/23	140	Pivetta - Water
143	Install Water Line Services and Meters	0 d	0 d	0 d	Thu 6/1/23	Thu 6/1/23	Thu 6/1/23	Thu 6/1/23	Thu 6/1/23	Thu 6/1/23	142	Pivetta - Water
144	Install Hydrants	8 d	0 d	0 d	Thu 6/1/23	Wed 10/11/23	Thu 6/1/23	Wed 10/11/23	Thu 6/1/23	Wed 10/11/23	143	Pivetta - Water
145	Abandon/Remove Existing Water Line	2 d	0 d	0 d	Thu 10/12/23	Fri 10/13/23	Thu 10/12/23	Fri 10/13/23	Thu 10/12/23	Fri 10/13/23	144	Pivetta - Water
146	**Water Line - Crossing - Taco Time to S. 2nd St. - Sta 18+49.0 & 18+49.0 to 19+31.9**	**219 d**	**0 d**	**0 d**	**Thu 3/30/23**	**Thu 2/29/24**	**Thu 3/30/23**	**Thu 2/29/24**	**Thu 3/30/23**	**Thu 2/29/24**		
147	Install Water Line and Appurtenances	2 d	0 d	0 d	Thu 5/11/23	Tue 5/23/23	Thu 5/11/23	Tue 5/23/23	Thu 5/11/23	Tue 5/23/23	140SS+5 d	Pivetta - Water
148	Cathodic Protection Submittal (Submittal #81, RAM 055)	0 d	0 d	0 d	Thu 3/30/23	Thu 3/30/23	Thu 3/30/23	Thu 3/30/23	Thu 3/30/23	Thu 3/30/23		
149	Test Station Changes (PCO-019 for RFI-70 and RFI-085 Changes)	10 d	0 d	0 d	Thu 7/13/23	Fri 10/13/23	Thu 7/13/23	Fri 10/13/23	Thu 7/13/23	Fri 10/13/23		
150	Procure Cathodic Protection	13 d	0 d	0 d	Mon 10/16/23	Wed 11/1/23	Mon 10/16/23	Wed 11/1/23	Mon 10/16/23	Wed 11/1/23	148,149	
151	Install Cathodic Protection over SPU Lines	4 d	0 d	0 d	Mon 2/26/24	Thu 2/29/24	Mon 2/26/24	Thu 2/29/24	Mon 2/26/24	Thu 2/29/24	147,150	Pivetta - Water
152	**Stage 2, Bypass, Cut and Cap**	**125 d**	**0 d**	**0 d**	**Mon 4/17/23**	**Fri 10/13/23**	**Mon 4/17/23**	**Fri 10/13/23**	**Mon 4/17/23**	**Fri 10/13/23**		
153	Install Water Bypass - Hertz/Lyft to Wendy's - Sta 15+55 to 16+40 (Performed with Stage 1)	0 d	0 d	0 d	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	Mon 4/17/23	143,147,145	Pivetta - Water
154	Install Water Bypass - Taco Time - Sta 18+25 to 18+50 (Deleted - Work Not Required)	1 d	0 d	0 d	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23	Mon 10/2/23		Pivetta - Water
155	Install Water Bypass - Buddy's Home Furnishing to Royal Orchid - Sta 21+00 to 24+80	5 d	0 d	0 d	Thu 10/5/23	Wed 10/11/23	Thu 10/5/23	Wed 10/11/23	Thu 10/5/23	Wed 10/11/23	143	Pivetta - Water
156	Cut and Cap - Chevron to S. Tobin Crossing - Sta 28+75 (Not Required)	1 d	0 d	0 d	Thu 10/12/23	Thu 10/12/23	Thu 10/12/23	Thu 10/12/23	Thu 10/12/23	Thu 10/12/23	155	Pivetta - Water
157	Cut and Cap Existing Water Line - McDonalds to Arco - Sta 30+60 to 34+10 (Not Required)	1 d	0 d	0 d	Fri 10/13/23	Fri 10/13/23	Fri 10/13/23	Fri 10/13/23	Fri 10/13/23	Fri 10/13/23	156	Pivetta - Water
158	**Water Line - Stage 2 - S. 3rd St. - Sta 203+40 to NW 3rd Pl - Sta 699+16.40**	**77 d**	**0 d**	**0 d**	**Mon 10/16/23**	**Thu 2/22/24**	**Mon 10/16/23**	**Thu 2/22/24**	**Mon 10/16/23**	**Thu 2/22/24**		
159	Install Water Line and Appurtenances	28.87 d	0 d	0 d	Mon 10/16/23	Wed 1/24/24	Mon 10/16/23	Wed 1/24/24	Mon 10/16/23	Wed 1/24/24	157,153	Pivetta - Water
160	FRPCS Concrete DMB	47 d	0 d	0 d	Thu 11/2/23	Wed 1/24/24	Thu 11/2/23	Wed 1/24/24	Thu 11/2/23	Wed 1/24/24	159	Pivetta - Water
161	Install Polypig Station	46 d	0 d	0 d	Thu 11/2/23	Wed 1/24/24	Thu 11/2/23	Wed 1/24/24	Thu 11/2/23	Wed 1/24/24	160	Pivetta - Water
162	Pressure Testing, Polypig, Disinfect Water Line	21 d	0 d	0 d	Wed 1/17/24	Thu 2/22/24	Wed 1/17/24	Thu 2/22/24	Wed 1/17/24	Thu 2/22/24	161	Pivetta - Water
163	Install Water Line Services and Meters	0 d	0 d	0 d	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	162	Pivetta - Water
164	Install Hydrants	0 d	0 d	0 d	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	163	Pivetta - Water
165	Abandon/Remove Existing Water Line	30 d	0 d	0 d	Mon 10/16/23	Thu 11/30/23	Mon 10/16/23	Thu 11/30/23	Mon 10/16/23	Thu 11/30/23	164	Pivetta - Water
166	**Stage 3 Bypass, Cut and Cap**	**3 d**	**399 d**	**399 d**	**NA**	**NA**	**Mon 4/1/24**	**Wed 4/3/24**	**Thu 11/6/25**	**Mon 11/10/25**		
167	Cut and Cap - Formula 1 Fast Lube to S. Tobin St. - Sta 25+65 to 28+65 (DELETED)	3 d	399 d	399 d	NA	NA	Mon 4/1/24	Wed 4/3/24	Thu 11/6/25	Mon 11/10/25		Pivetta - Water/City of Renton Wat
168	**Water Line - Stage 3 - S. Tobin St. - Sta 28+58.6 to 28+61.6 (Performing with Stage 2)**	**63 d**	**0 d**	**0 d**	**Mon 11/6/23**	**Thu 2/22/24**	**Mon 11/6/23**	**Thu 2/22/24**	**Mon 11/6/23**	**Thu 2/22/24**		
169	Install Water Line and Appurtenances	4 d	0 d	0 d	Mon 11/6/23	Thu 11/9/23	Mon 11/6/23	Thu 11/9/23	Mon 11/6/23	Thu 11/9/23	44	Pivetta - Water
170	Pressure Testing, Polypig, Disinfect Water Line	22 d	0 d	0 d	Wed 1/17/24	Thu 2/22/24	Wed 1/17/24	Thu 2/22/24	Wed 1/17/24	Thu 2/22/24	169	Pivetta - Water
171	Install Water Line Services and Meters	4 d	0 d	0 d	Mon 1/8/24	Wed 1/24/24	Mon 1/8/24	Wed 1/24/24	Mon 1/8/24	Wed 1/24/24	170	Pivetta - Water
172	Install Hydrants	0 d	0 d	0 d	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	Mon 1/8/24	171	Pivetta - Water
173	Abandon/Remove Existing Water Line and Bypass	30 d	0 d	0 d	Tue 1/9/24	Thu 2/22/24	Tue 1/9/24	Thu 2/22/24	Tue 1/9/24	Thu 2/22/24	172	Pivetta - Water
174	**Install Hydrants in Conflict**	**168 d**	**69 d**	**69 d**	**NA**	**NA**	**Wed 6/12/24**	**Thu 2/20/25**	**Tue 12/3/24**	**Thu 5/29/25**		
175	Hydrant at Walgreens (STA 16+54) - Sewer Conflict (RFI078)	1 d	118 d	48 d	NA	NA	Wed 6/12/24	Wed 6/12/24	Tue 12/3/24	Tue 12/3/24	185	
176	Hydrant at NE corner of Rainier & S 2nd St - Reinstall (RFI139) - after JUT removal	1 d	203 d	202 d	NA	NA	Wed 7/31/24	Wed 7/31/24	Thu 5/29/25	Thu 5/29/25	127	
177	Blow Off at Gene Meyer (STA 20+25) - JUT/Storm Conflict/Sequence	1 d	85 d	15 d	NA	NA	Wed 7/31/24	Wed 7/31/24	Tue 12/3/24	Tue 12/3/24	127,208	

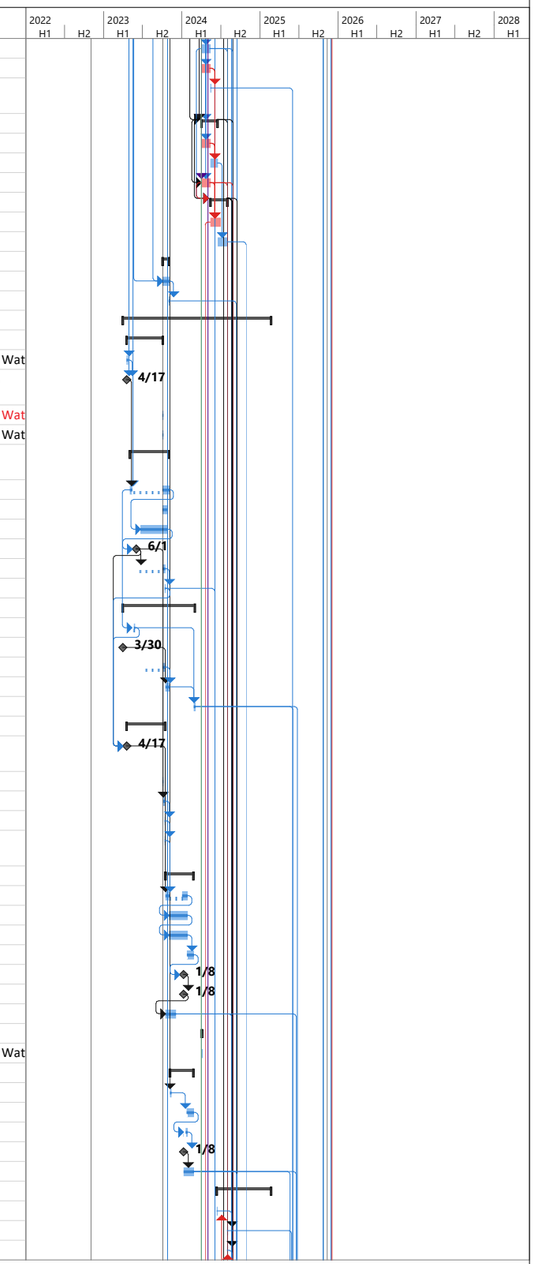

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
178	Hydrant at Autozone (STA 21+73) - JUT Conflict	1 d	85 d	15 d	NA	NA	Wed 7/31/24	Wed 7/31/24	Tue 12/3/24	Tue 12/3/24	127	
179	Hydrant at Watson (STA 24+24) - JUT Conflict	1 d	85 d	15 d	NA	NA	Wed 7/31/24	Wed 7/31/24	Tue 12/3/24	Tue 12/3/24	127	
180	Hydrant at Tommy's Café (STA 26+27.5) - adjust length after stg 1 chan	1 d	69 d	68 d	NA	NA	Thu 2/20/25	Thu 2/20/25	Thu 5/29/25	Thu 5/29/25	374	
181	**Sewer - Sta 15+49.20 to 42+77.80**	**117 d**	**97 d**	**97 d**	**Tue 1/30/24**	**NA**	**Tue 1/30/24**	**Mon 7/15/24**	**Tue 1/30/24**	**Tue 12/3/24**		
182	L035 - PCO033 Sewer Bypass (sent 1/30/24) - Response/Resolution	0 d	44 d	44 d	Tue 1/30/24	NA	Tue 1/30/24	Mon 4/1/24	Tue 1/30/24	Mon 6/3/24		
183	**Sewer - Night (Walgreens to Sansonina) - Sta 15+49.20 to 18+26.81**	**7 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 6/3/24**	**Tue 6/11/24**	**Mon 6/3/24**	**Tue 6/11/24**		
184	Remove/Replace Manholes and Install Sewer	5 d	0 d	0 d	NA	NA	Mon 6/3/24	Fri 6/7/24	Mon 6/3/24	Fri 6/7/24	145,39,107,182,128SS+14 d	Pivetta - Sewer
185	Install New Side Sewer	2 d	0 d	0 d	NA	NA	Mon 6/10/24	Tue 6/11/24	Mon 6/10/24	Tue 6/11/24	184	Pivetta - Sewer
186	**Sewer (Big Island Poke to Hayes Pl SW) - Sta 19+63.58 to 25+43.57**	**5 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 6/12/24**	**Tue 6/18/24**	**Wed 6/12/24**	**Tue 6/18/24**		
187	Remove/Replace Manholes	5 d	0 d	0 d	NA	NA	Wed 6/12/24	Tue 6/18/24	Wed 6/12/24	Tue 6/18/24	185	Pivetta - Sewer
188	**S. 2nd St. - Sta 19+64.16**	**3 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 6/20/24**	**Mon 6/24/24**	**Thu 6/20/24**	**Mon 6/24/24**		
189	Install Sewer and Manholes	3 d	0 d	0 d	NA	NA	Thu 6/20/24	Mon 6/24/24	Thu 6/20/24	Mon 6/24/24	187	Pivetta - Sewer
190	**Sewer (Chevron to Advance Auto Tune) - Sta 28+55.98 to 42+77.80**	**10 d**	**70 d**	**70 d**	**NA**	**NA**	**Tue 6/25/24**	**Tue 7/9/24**	**Thu 10/3/24**	**Wed 10/16/24**		
191	Remove/Replace/Install Manholes	7 d	70 d	0 d	NA	NA	Tue 6/25/24	Wed 7/3/24	Thu 10/3/24	Fri 10/11/24	189	Pivetta - Sewer
192	Install Sewer	3 d	70 d	0 d	NA	NA	Fri 7/5/24	Tue 7/9/24	Mon 10/14/24	Wed 10/16/24	191	Pivetta - Sewer
193	**Sewer - Night/Side Street - SW Victoria - Sta 24+91.19**	**1 d**	**70 d**	**70 d**	**NA**	**NA**	**Wed 7/10/24**	**Wed 7/10/24**	**Thu 10/17/24**	**Thu 10/17/24**		
194	Remove/Replace Manholes	1 d	70 d	0 d	NA	NA	Wed 7/10/24	Wed 7/10/24	Thu 10/17/24	Thu 10/17/24	192	Pivetta - Sewer
195	**Sewer - Night/Side Street - Hayes Pl SW - Sta 25+43.57**	**1 d**	**70 d**	**70 d**	**NA**	**NA**	**Thu 7/11/24**	**Thu 7/11/24**	**Fri 10/18/24**	**Fri 10/18/24**		
196	Remove/Replace/Install Manholes	1 d	70 d	0 d	NA	NA	Thu 7/11/24	Thu 7/11/24	Fri 10/18/24	Fri 10/18/24	194	Pivetta - Sewer
197	**Sewer - Night/Renton Ave Ext - Sta 32+81.14 to 31+60.06**	**2 d**	**70 d**	**70 d**	**NA**	**NA**	**Fri 7/12/24**	**Mon 7/15/24**	**Mon 10/21/24**	**Tue 12/3/24**		
198	Remove/Replace/Install Manholes	1 d	70 d	0 d	NA	NA	Fri 7/12/24	Fri 7/12/24	Mon 10/21/24	Mon 10/21/24	196	Pivetta - Sewer
199	Install Sewer	1 d	97 d	27 d	NA	NA	Mon 7/15/24	Mon 7/15/24	Tue 12/3/24	Tue 12/3/24	198	Pivetta - Sewer
200	**Install CIPP Lining**	**28 d**	**70 d**	**70 d**	**NA**	**NA**	**Mon 7/15/24**	**Wed 8/21/24**	**Tue 10/22/24**	**Tue 12/3/24**		
201	Install CIPP Lining (Big Island Poke to Hayes Pl SW) - Sta 19+63.58 to 25+43.57	4 d	70 d	0 d	NA	NA	Mon 7/15/24	Thu 7/18/24	Tue 10/22/24	Fri 10/25/24	37,198	Insituform
202	Install CIPP Lining (Chevron to Advance Auto Tune) - Sta 28+55.98 to 42+77.80	9 d	70 d	0 d	NA	NA	Fri 7/19/24	Wed 7/31/24	Mon 10/28/24	Thu 11/7/24	201,191	Insituform
203	Install CIPP Lining (SW Victoria) - Sta 24+91.19	5 d	70 d	0 d	NA	NA	Thu 8/1/24	Wed 8/7/24	Fri 11/8/24	Fri 11/15/24	202,194	Insituform
204	Install CIPP Lining (Hayes Pl SW) - Sta 25+43.57	5 d	70 d	0 d	NA	NA	Thu 8/8/24	Wed 8/14/24	Mon 11/18/24	Fri 11/22/24	203,196	Insituform
205	Install CIPP Lining (Renton Ave Ext) - Sta 32+81.14 to 31+60.06	5 d	70 d	0 d	NA	NA	Thu 8/15/24	Wed 8/21/24	Mon 11/25/24	Tue 12/3/24	198,204	Insituform
206	**Storm Drainage - Sta 15+11.89 to 41+02.35**	**57 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 6/25/24**	**Fri 9/13/24**	**Tue 6/25/24**	**Mon 11/10/25**		
207	**Storm Drainage (Walgreens to Sansonina) - Sta 15+11.89 to 17+63.75**	**12 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 6/25/24**	**Thu 7/11/24**	**Tue 6/25/24**	**Thu 7/11/24**		
208	Install Drainage and Catch Basins	10 d	0 d	0 d	NA	NA	Tue 6/25/24	Tue 7/9/24	Tue 6/25/24	Tue 7/9/24	189	Pivetta - Storm
209	**Storm Drainage - Night/Crossing - Sta 16+05.52**	**2 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 7/10/24**	**Thu 7/11/24**	**Wed 7/10/24**	**Thu 7/11/24**		
210	Install Drainage and Catch Basins	2 d	0 d	0 d	NA	NA	Wed 7/10/24	Thu 7/11/24	Wed 7/10/24	Thu 7/11/24	208	Pivetta - Storm
211	**Storm Drainage (Big Island Poke to Watson Security) - Sta 18+54.92 to 23+32.67**	**24 d**	**0 d**	**0 d**	**NA**	**NA**	**Fri 7/12/24**	**Wed 8/14/24**	**Fri 7/12/24**	**Mon 11/10/25**		
212	Install Drainage and Catch Basins	13 d	0 d	0 d	NA	NA	Fri 7/12/24	Tue 7/30/24	Fri 7/12/24	Tue 7/30/24	210	Pivetta - Storm
213	**Storm Drainage - S. 2nd St. - Night/Crossings, Stage 2 and 3 Work - Sta 19+07.53 to 22+07.86**	**11 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 7/31/24**	**Wed 8/14/24**	**Wed 7/31/24**	**Mon 11/10/25**		
214	Install Drainage and Catch Basins	10 d	0 d	0 d	NA	NA	Wed 7/31/24	Tue 8/13/24	Wed 7/31/24	Tue 8/13/24	210,212	Pivetta - Storm
215	Install Filterra Unit	1 d	307 d	307 d	NA	NA	Wed 8/14/24	Wed 8/14/24	Mon 11/10/25	Mon 11/10/25	214	Pivetta - Storm
216	**Storm Drainage - SW Victoria St. to Brown Bear Car Wash- Night/Crossing - Sta 24+70.79 to 26+65.08**	**8 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 8/14/24**	**Fri 8/23/24**	**Wed 8/14/24**	**Fri 8/23/24**		
217	Install Drainage and Catch Basins	8 d	0 d	0 d	NA	NA	Wed 8/14/24	Fri 8/23/24	Wed 8/14/24	Fri 8/23/24	214,127	Pivetta - Storm
218	**Storm Drainage Brown Bear to Renton Laundry - Sta 26+65.08 to 35+53.35**	**29 d**	**14 d**	**14 d**	**NA**	**NA**	**Wed 7/31/24**	**Tue 9/10/24**	**Tue 8/20/24**	**Mon 9/22/25**		
219	Install Drainage and Catch Basins	11 d	14 d	0 d	NA	NA	Wed 7/31/24	Wed 8/14/24	Tue 8/20/24	Wed 9/4/24	212,114,117,120,123,126	Pivetta - Storm
220	Install Filterra Units	3 d	269 d	0 d	NA	NA	Thu 8/15/24	Mon 8/19/24	Thu 9/18/25	Mon 9/22/25	219	Pivetta - Storm
221	**Storm Drainage - Renton Ave Ext - Night/Crossing - Sta 31+39.02 to 33+02.08**	**11 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 8/26/24**	**Tue 9/10/24**	**Mon 8/26/24**	**Tue 9/10/24**		
222	Install Drainage and Catch Basins	11 d	0 d	0 d	NA	NA	Mon 8/26/24	Tue 9/10/24	Mon 8/26/24	Tue 9/10/24	217,114,117,120,123,126	Pivetta - Storm
223	**Storm Drainage Mathewson's Automotive to Judo Boxing - Sta 37+84.90 to 41+02.35**	**4 d**	**14 d**	**14 d**	**NA**	**NA**	**Thu 8/15/24**	**Tue 8/20/24**	**Thu 9/5/24**	**Tue 9/10/24**		
224	Install Drainage and Catch Basins	4 d	14 d	14 d	NA	NA	Thu 8/15/24	Tue 8/20/24	Thu 9/5/24	Tue 9/10/24	219	Pivetta - Storm
225	**Storm Drainage - NW 3rd Pl - Night/Crossing - Sta 40+68.75 to 41+02.35**	**3 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 9/11/24**	**Fri 9/13/24**	**Wed 9/11/24**	**Fri 9/13/24**		
226	Install Drainage and Catch Basins	3 d	0 d	0 d	NA	NA	Wed 9/11/24	Fri 9/13/24	Wed 9/11/24	Fri 9/13/24	224,222,132,129FF	Pivetta - Storm
227	**Decorative Illumination System - Sta 14+89 to 41+55**	**167 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 4/1/24**	**Tue 11/26/24**	**Thu 6/13/24**	**Tue 11/26/24**		
228	**Below Grade**	**42 d**	**52 d**	**52 d**	**NA**	**NA**	**Mon 4/1/24**	**Wed 5/29/24**	**Thu 6/13/24**	**Fri 9/13/24**		
229	Trench and Conduit	23 d	52 d	0 d	NA	NA	Mon 4/1/24	Wed 5/1/24	Thu 6/13/24	Wed 7/17/24		Golden Gate
230	Foundations	24 d	74 d	0 d	NA	NA	Mon 4/1/24	Thu 5/2/24	Wed 7/17/24	Mon 8/19/24	61,229SS	Golden Gate
231	Junction Boxes	18 d	74 d	0 d	NA	NA	Fri 5/3/24	Wed 5/29/24	Tue 8/20/24	Fri 9/13/24	230,110	Golden Gate
232	Service Installation	10 d	98 d	98 d	NA	NA	Fri 5/17/24	Fri 5/31/24	Tue 10/8/24	Mon 10/21/24	231SS+10 d	Golden Gate/PSE - Electric
233	**Above Ground**	**162 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 4/8/24**	**Tue 11/26/24**	**Thu 8/22/24**	**Tue 11/26/24**		
234	Install Lighting Wiring	20 d	0 d	0 d	NA	NA	Tue 10/22/24	Tue 11/19/24	Tue 10/22/24	Tue 11/19/24	231,232,345	Golden Gate
235	Set Poles	62 d	95 d	95 d	NA	NA	Mon 4/8/24	Fri 7/5/24	Thu 8/22/24	Tue 11/19/24	230SS+5 d	Golden Gate
236	Test and Turn On	2 d	0 d	0 d	NA	NA	Wed 11/20/24	Thu 11/21/24	Wed 11/20/24	Thu 11/21/24	235,234	Golden Gate
237	Remove and Salvage Old Poles&Wiring	3 d	0 d	0 d	NA	NA	Fri 11/22/24	Tue 11/26/24	Fri 11/22/24	Tue 11/26/24	236	Golden Gate

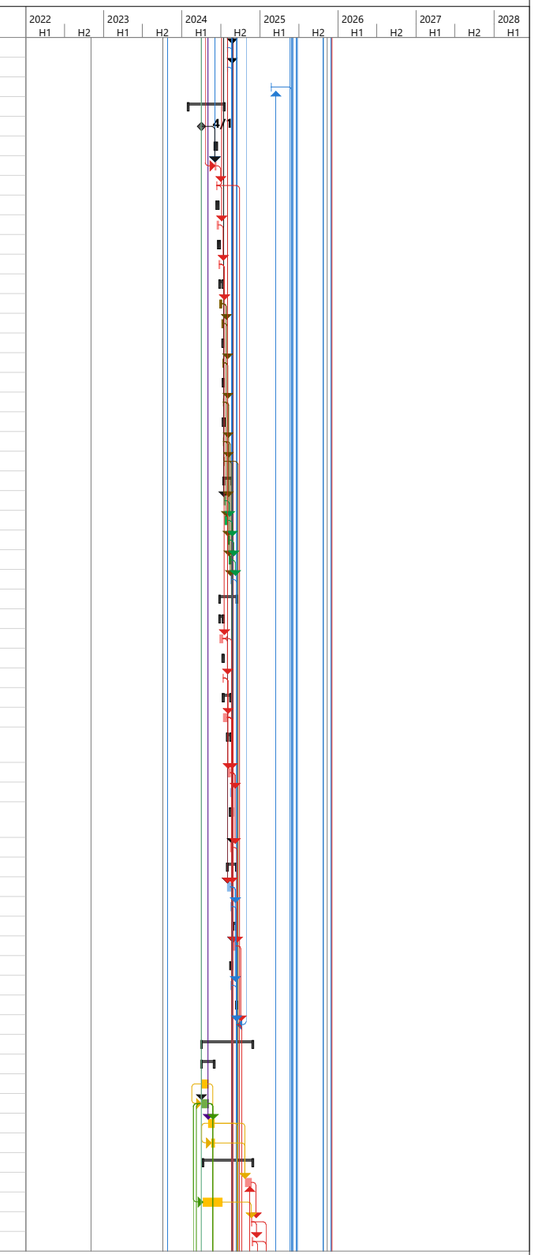

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
238	**Signalization - Sta 14+10 to 40+40**	**192 d**	**52 d**	**52 d**	**NA**	**NA**	**Thu 5/2/24**	**Thu 2/13/25**	**Thu 7/18/24**	**Mon 11/10/25**		
239	**Traffic Signal Rainier & SW Sunset - Sta 14+10**	**157 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 5/2/24**	**Tue 12/17/24**	**Thu 7/18/24**	**Tue 12/17/24**		
240	**Below Grade**	**8 d**	**52 d**	**52 d**	**NA**	**NA**	**Thu 5/2/24**	**Mon 5/13/24**	**Thu 7/18/24**	**Tue 12/3/24**		
241	Conduit Underground	5 d	52 d	0 d	NA	NA	Thu 5/2/24	Wed 5/8/24	Thu 7/18/24	Wed 7/24/24	229	Golden Gate
242	Foundations - before C&G	3 d	143 d	0 d	NA	NA	Fri 5/3/24	Tue 5/7/24	Wed 11/27/24	Tue 12/3/24	230	Golden Gate
243	Road Crossings	3 d	52 d	0 d	NA	NA	Thu 5/9/24	Mon 5/13/24	Thu 7/25/24	Mon 7/29/24	241	Golden Gate
244	Service Installation	1 d	0 d	0 d	NA	NA	Tue 12/3/24	Tue 12/3/24	Tue 12/3/24	Tue 12/3/24	246	Golden Gate/PSE - Electric
245	**Above Ground**	**13 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 11/27/24**	**Tue 12/17/24**	**Wed 11/27/24**	**Tue 12/17/24**		
246	Install Boxes - after C&G/Sidewalks	2 d	0 d	0 d	NA	NA	Wed 11/27/24	Mon 12/2/24	Wed 11/27/24	Mon 12/2/24	243,237	Golden Gate
247	Pull Cable	2 d	0 d	0 d	NA	NA	Wed 12/4/24	Thu 12/5/24	Wed 12/4/24	Thu 12/5/24	244	Golden Gate
248	Build Traffic Signal System	8 d	0 d	0 d	NA	NA	Fri 12/6/24	Tue 12/17/24	Fri 12/6/24	Tue 12/17/24	247,242	Golden Gate
249	**Traffic Signal Rainier & 2nd Street**	**163 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 5/8/24**	**Wed 1/8/25**	**Tue 7/30/24**	**Wed 1/8/25**		
250	**Below Grade**	**14 d**	**56 d**	**56 d**	**NA**	**NA**	**Wed 5/8/24**	**Tue 5/28/24**	**Tue 7/30/24**	**Thu 12/19/24**		
251	Foundations	3 d	152 d	0 d	NA	NA	Wed 5/8/24	Fri 5/10/24	Tue 12/17/24	Thu 12/19/24	242	Golden Gate
252	Conduit Underground	5 d	52 d	0 d	NA	NA	Tue 5/14/24	Mon 5/20/24	Tue 7/30/24	Mon 8/5/24	243	Golden Gate
253	Road Crossings	3 d	52 d	0 d	NA	NA	Tue 5/21/24	Thu 5/23/24	Tue 8/6/24	Thu 8/8/24	252	Golden Gate
254	Install Boxes	2 d	52 d	0 d	NA	NA	Fri 5/24/24	Tue 5/28/24	Fri 8/9/24	Mon 8/12/24	253	Golden Gate
255	Service Installation	1 d	138 d	138 d	NA	NA	Wed 5/29/24	Wed 5/29/24	Tue 12/17/24	Tue 12/17/24	254	Golden Gate/PSE - Electric
256	**Above Ground**	**10 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 12/18/24**	**Wed 1/8/25**	**Wed 12/18/24**	**Wed 1/8/25**		
257	Pull Cable	2 d	0 d	0 d	NA	NA	Wed 12/18/24	Thu 12/19/24	Wed 12/18/24	Thu 12/19/24	248,255	Golden Gate
258	Build Traffic Signal System	8 d	0 d	0 d	NA	NA	Fri 12/20/24	Wed 1/8/25	Fri 12/20/24	Wed 1/8/25	257	Golden Gate
259	**Pedestrian Signal Rainier& SW Victoria**	**179 d**	**63 d**	**63 d**	**NA**	**NA**	**Mon 5/13/24**	**Wed 2/5/25**	**Tue 8/13/24**	**Fri 10/31/25**		
260	**Below Grade**	**15 d**	**63 d**	**63 d**	**NA**	**NA**	**Mon 5/13/24**	**Mon 6/3/24**	**Tue 8/13/24**	**Fri 12/20/24**		
261	Foundations	1 d	152 d	0 d	NA	NA	Mon 5/13/24	Mon 5/13/24	Fri 12/20/24	Fri 12/20/24	251	Golden Gate
262	Conduit Underground	2 d	52 d	0 d	NA	NA	Wed 5/29/24	Thu 5/30/24	Tue 8/13/24	Wed 8/14/24	254	Golden Gate
263	Road Crossings	1 d	52 d	0 d	NA	NA	Fri 5/31/24	Fri 5/31/24	Thu 8/15/24	Thu 8/15/24	262	Golden Gate
264	Install Boxes	1 d	52 d	0 d	NA	NA	Mon 6/3/24	Mon 6/3/24	Fri 8/16/24	Fri 8/16/24	263	Golden Gate
265	Service Installation	1 d	344 d	157 d	NA	NA	Tue 6/4/24	Tue 6/4/24	Thu 10/23/25	Thu 10/23/25	264	Golden Gate/PSE - Electric
266	**Above Ground**	**6 d**	**187 d**	**187 d**	**NA**	**NA**	**Wed 1/29/25**	**Wed 2/5/25**	**Fri 10/24/25**	**Fri 10/31/25**		
267	Pull cable	2 d	187 d	0 d	NA	NA	Wed 1/29/25	Thu 1/30/25	Fri 10/24/25	Mon 10/27/25	258,265,278	Golden Gate
268	Build Traffic Signal System	4 d	187 d	0 d	NA	NA	Fri 1/31/25	Wed 2/5/25	Tue 10/28/25	Fri 10/31/25	267,251	Golden Gate
269	**Traffic Signal Rainier& Renton Ave Ext**	**172 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 5/14/24**	**Tue 1/28/25**	**Mon 8/19/24**	**Tue 1/28/25**		
270	**Below Grade**	**27 d**	**66 d**	**66 d**	**NA**	**NA**	**Tue 5/14/24**	**Fri 6/21/24**	**Mon 8/19/24**	**Mon 1/13/25**		
271	Foundations	10 d	152 d	0 d	NA	NA	Tue 5/14/24	Tue 5/28/24	Mon 12/23/24	Mon 1/13/25	261	Golden Gate
272	Conduit Underground	8 d	52 d	0 d	NA	NA	Tue 6/4/24	Thu 6/13/24	Mon 8/19/24	Wed 8/28/24	264	Golden Gate
273	Road Crossings	3 d	52 d	0 d	NA	NA	Fri 6/14/24	Tue 6/18/24	Thu 8/29/24	Tue 9/3/24	272	Golden Gate
274	Install Boxes	2 d	52 d	0 d	NA	NA	Thu 6/20/24	Fri 6/21/24	Wed 9/4/24	Thu 9/5/24	273	Golden Gate
275	Service Installation	1 d	131 d	131 d	NA	NA	Mon 6/24/24	Mon 6/24/24	Wed 1/8/25	Wed 1/8/25	274	Golden Gate/PSE - Electric
276	**Above Ground**	**13 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 1/9/25**	**Tue 1/28/25**	**Thu 1/9/25**	**Tue 1/28/25**		
277	Pull Cable	3 d	0 d	0 d	NA	NA	Thu 1/9/25	Mon 1/13/25	Thu 1/9/25	Mon 1/13/25	275,258	Golden Gate
278	Build Traffic Signal System	10 d	0 d	0 d	NA	NA	Tue 1/14/25	Tue 1/28/25	Tue 1/14/25	Tue 1/28/25	277,261,271	Golden Gate
279	**Pedestrian Signal Rainier& 3rd Pl**	**174 d**	**69 d**	**69 d**	**NA**	**NA**	**Wed 5/29/24**	**Thu 2/13/25**	**Fri 9/6/24**	**Mon 11/10/25**		
280	**Below Grade**	**23 d**	**69 d**	**69 d**	**NA**	**NA**	**Wed 5/29/24**	**Mon 7/1/24**	**Fri 9/6/24**	**Mon 11/3/25**		
281	Foundations	1 d	355 d	168 d	NA	NA	Wed 5/29/24	Wed 5/29/24	Mon 11/3/25	Mon 11/3/25	271	Golden Gate
282	Conduit Underground	3 d	52 d	0 d	NA	NA	Mon 6/24/24	Wed 6/26/24	Fri 9/6/24	Tue 9/10/24	274	Golden Gate
283	Road Crossings	2 d	52 d	0 d	NA	NA	Thu 6/27/24	Fri 6/28/24	Wed 9/11/24	Thu 9/12/24	282	Golden Gate
284	Install Boxes	1 d	52 d	0 d	NA	NA	Mon 7/1/24	Mon 7/1/24	Fri 9/13/24	Fri 9/13/24	283	Golden Gate
285	Service Installation	1 d	331 d	144 d	NA	NA	Tue 7/2/24	Tue 7/2/24	Fri 10/31/25	Fri 10/31/25	284	Golden Gate/PSE - Electric
286	**Above Ground**	**6 d**	**187 d**	**187 d**	**NA**	**NA**	**Thu 2/6/25**	**Thu 2/13/25**	**Mon 11/3/25**	**Mon 11/10/25**		
287	Pull Cable	1 d	187 d	0 d	NA	NA	Thu 2/6/25	Thu 2/6/25	Mon 11/3/25	Mon 11/3/25	285,268	Golden Gate
288	Build Traffic Signal System	5 d	187 d	187 d	NA	NA	Fri 2/7/25	Thu 2/13/25	Tue 11/4/25	Mon 11/10/25	281,287	Golden Gate
289	**Walls - Sta 15+50.95 to 799+17.37**	**231 d**	**284 d**	**284 d**	**Mon 10/2/23**	**NA**	**Mon 10/2/23**	**Tue 9/17/24**	**Mon 10/2/23**	**Mon 11/10/25**		
290	**Wall 1 - Modular Block FW - Sta 15+50.95 to 16+21.24 (Wall Sta 0+00 to 1+18)**	**25 d**	**91 d**	**91 d**	**NA**	**NA**	**Mon 4/8/24**	**Fri 5/10/24**	**Fri 8/16/24**	**Thu 11/6/25**		
291	Constuct Modular Block Fill Wall - Wall 1	15 d	91 d	0 d	NA	NA	Mon 4/8/24	Fri 4/26/24	Fri 8/16/24	Fri 9/6/24	230SS+5 d	Key West
292	FRPCS Thickened Edge Sidewalk	5 d	370 d	0 d	NA	NA	Mon 4/29/24	Fri 5/3/24	Fri 10/24/25	Thu 10/30/25	291	WCCI
293	Install Pedestrian Railing	5 d	370 d	16 d	NA	NA	Mon 5/6/24	Fri 5/10/24	Fri 10/31/25	Thu 11/6/25	292	WCCI
294	**Wall 2 - Modular Block FW - Sta 17+08.50 to 17+23.95 (Wall Sta 0+00 to 0+59)**	**10 d**	**91 d**	**91 d**	**NA**	**NA**	**Mon 4/29/24**	**Fri 5/10/24**	**Mon 9/9/24**	**Mon 11/10/25**		
295	Construct Modular Block Fill Wall - Wall 2	5 d	91 d	0 d	NA	NA	Mon 4/29/24	Fri 5/3/24	Mon 9/9/24	Fri 9/13/24	291	Key West
296	FRPCS Thickened Edge Sidewalk	5 d	372 d	372 d	NA	NA	Mon 5/6/24	Fri 5/10/24	Tue 11/4/25	Mon 11/10/25	295,292SS	WCCI
297	**Wall 5 - CCFW & CIP Fill Wall - Sta 399+50.72 to 399+39.01 (Wall Sta 0+00 to 0+35)**	**161 d**	**354 d**	**354 d**	**Mon 10/2/23**	**NA**	**Mon 10/2/23**	**Thu 6/6/24**	**Mon 10/2/23**	**Mon 11/10/25**		
298	Demolish Existing Wall 5 - Sta 0+10 to 0+21.70	2 d	0 d	0 d	Mon 10/2/23	Tue 10/3/23	Mon 10/2/23	Tue 10/3/23	Mon 10/2/23	Tue 10/3/23	83	Pivetta
299	Construct CIP Fill Wall - Wall 5	15 d	75 d	0 d	NA	NA	Tue 4/23/24	Mon 5/13/24	Fri 8/9/24	Thu 8/29/24	230SS+16 d,298	WCCI

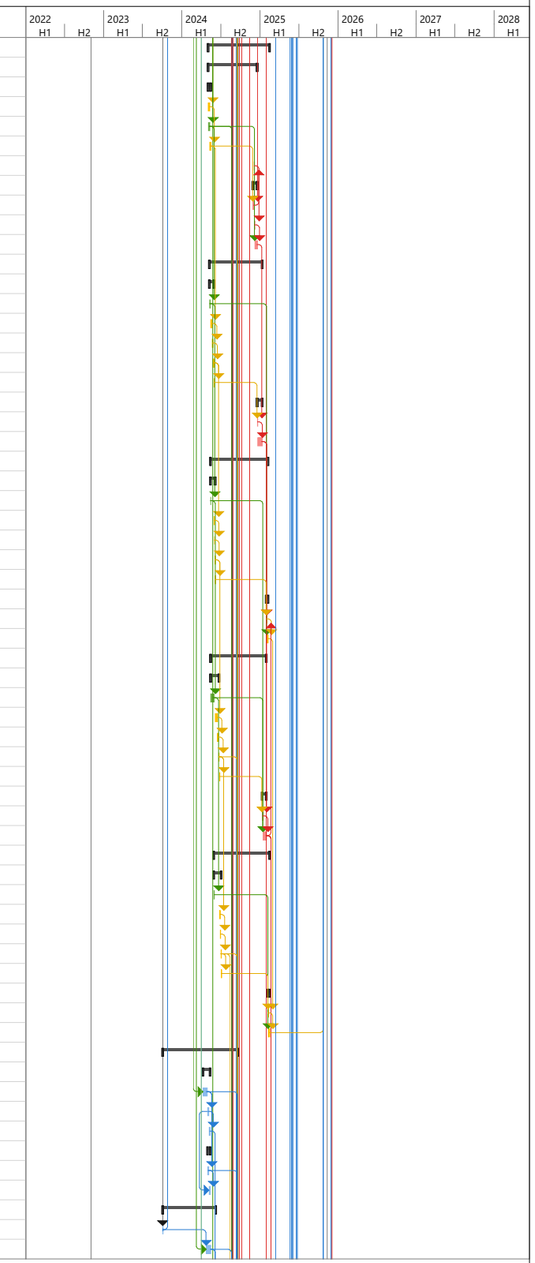

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
300	Construct Cement Concrete Fill Wall - Wall 5	10 d	75 d	0 d	NA	NA	Tue 5/14/24	Tue 5/28/24	Fri 8/30/24	Fri 9/13/24	230,299	WCCI
301	Construct WSDOT Std 4"Thick Gutter - Wall 5	5 d	354 d	0 d	NA	NA	Wed 5/29/24	Tue 6/4/24	Fri 10/31/25	Thu 11/6/25	300	WCCI
302	Install Pedestrian Railing - Sta 0+10 to 0+35 - Wall 5	2 d	354 d	354 d	NA	NA	Wed 6/5/24	Thu 6/6/24	Fri 11/7/25	Mon 11/10/25	293,301	WCCI
303	**Wall 6 - Rock Wall - Sta 799+42.45 to 799+17.37 (Wall Sta 0+00 to 0+19.29)**	**5 d**	**111 d**	**111 d**	**NA**	**NA**	**Mon 4/1/24**	**Fri 4/5/24**	**Mon 9/9/24**	**Fri 9/13/24**		
304	Excavate/Construct/Backfill Rock Wall - Wall 6	5 d	111 d	111 d	NA	NA	Mon 4/1/24	Fri 4/5/24	Mon 9/9/24	Fri 9/13/24	94	Pivetta - Earthwork
305	**Gateway Wall A - Sta 33+59.15 to 599+37.00**	**20 d**	**269 d**	**269 d**	**NA**	**NA**	**Tue 8/20/24**	**Tue 9/17/24**	**Tue 9/23/25**	**Mon 10/20/25**		
306	Construct Gateway Wall A - Renton Ave. Ext.	15 d	269 d	0 d	NA	NA	Tue 8/20/24	Tue 9/10/24	Tue 9/23/25	Mon 10/13/25	220,299	WCCI
307	Install Decorative Cutouts and Skate Deterrent Gateway Wall A - Renton Ave. Ext.	5 d	269 d	266 d	NA	NA	Wed 9/11/24	Tue 9/17/24	Tue 10/14/25	Mon 10/20/25	306	WCCI
308	**Curb and Gutter - Sta 14+30.99 to 42+80.28**	**25 d**	**70 d**	**70 d**	**NA**	**NA**	**Thu 8/22/24**	**Thu 9/26/24**	**Wed 12/4/24**	**Mon 11/10/25**		
309	**Curb and Gutter - Walgreens to Big Island Poke - Sta 14+30.99 to 19+12.69**	**2 d**	**70 d**	**70 d**	**NA**	**NA**	**Thu 8/22/24**	**Fri 8/23/24**	**Wed 12/4/24**	**Mon 11/10/25**	**205,284**	
310	Grade/Prep Base/Place CSBC	1 d	70 d	0 d	NA	NA	Thu 8/22/24	Thu 8/22/24	Wed 12/4/24	Wed 12/4/24	208,242,165,52,107,175,177,178,179,	Pivetta - Earthwork
311	Form and Pour Curb and Gutter	1 d	300 d	300 d	NA	NA	Fri 8/23/24	Fri 8/23/24	Mon 11/10/25	Mon 11/10/25	310	WCCI
312	**Curb and Gutter - Big Island Poke to SW Victoria St - Sta 19+12.69 to 24+80**	**4 d**	**70 d**	**70 d**	**NA**	**NA**	**Fri 8/23/24**	**Wed 8/28/24**	**Thu 12/5/24**	**Mon 11/10/25**		
313	Grade/Prep Base/Place CSBC	2 d	70 d	0 d	NA	NA	Fri 8/23/24	Mon 8/26/24	Thu 12/5/24	Fri 12/6/24	310	Pivetta - Earthwork
314	Form and Pour Curb and Gutter	2 d	297 d	297 d	NA	NA	Tue 8/27/24	Wed 8/28/24	Fri 11/7/25	Mon 11/10/25	313	WCCI
315	**Curb and Gutter - SW Victoria St. to Renton Ave Ext. - Sta 25+00 to 31+64.76**	**17 d**	**70 d**	**70 d**	**NA**	**NA**	**Tue 8/27/24**	**Thu 9/19/24**	**Mon 12/9/24**	**Mon 11/10/25**		
316	Grade/Prep Base/Place CSBC	3 d	70 d	0 d	NA	NA	Tue 8/27/24	Thu 8/29/24	Mon 12/9/24	Wed 12/11/24	212,313	Pivetta - Earthwork
317	Form and Pour Curb and Gutter	3 d	70 d	0 d	NA	NA	Fri 8/30/24	Wed 9/4/24	Thu 12/12/24	Mon 12/16/24	316	WCCI
318	**Bus Shelter - Sta 27+45.48**	**11 d**	**282 d**	**282 d**	**NA**	**NA**	**Thu 9/5/24**	**Thu 9/19/24**	**Mon 10/27/25**	**Mon 11/10/25**		
319	FRPCS Bus Shelter Footings	10 d	282 d	0 d	NA	NA	Thu 9/5/24	Wed 9/18/24	Mon 10/27/25	Fri 11/7/25	317	WCCI
320	Install Bus Shelter	1 d	282 d	282 d	NA	NA	Thu 9/19/24	Thu 9/19/24	Mon 11/10/25	Mon 11/10/25	319	Pivetta
321	**Curb and Gutter - Renton Ave. Ext to End - Sta 32+56.87 to 42+80.28**	**5 d**	**61 d**	**61 d**	**NA**	**NA**	**Mon 9/16/24**	**Fri 9/20/24**	**Fri 12/13/24**	**Mon 11/10/25**		
322	Grade/Prep Base/Place CSBC	2 d	61 d	0 d	NA	NA	Mon 9/16/24	Tue 9/17/24	Fri 12/13/24	Mon 12/16/24	226,316	Pivetta - Earthwork
323	Form and Pour Curb and Gutter	2 d	61 d	0 d	NA	NA	Wed 9/18/24	Thu 9/19/24	Tue 12/17/24	Wed 12/18/24	322,317	WCCI
324	Install Curb Mounted Delineator Posts - Renton Ave. Ext.	1 d	281 d	281 d	NA	NA	Fri 9/20/24	Fri 9/20/24	Mon 11/10/25	Mon 11/10/25	323	SPM
325	**Islands - Sta 32+90 to 33+30**	**5 d**	**61 d**	**61 d**	**NA**	**NA**	**Fri 9/20/24**	**Thu 9/26/24**	**Thu 12/19/24**	**Thu 1/2/25**		
326	Grade/Place CSBC/Place Island 2 - Renton Ave Ext.	5 d	61 d	0 d	NA	NA	Fri 9/20/24	Thu 9/26/24	Thu 12/19/24	Thu 1/2/25	323,199	Pivetta - Earthwork
327	**Sidewalk - 14+30.99 to 42+80.28**	**36 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 9/16/24**	**Mon 11/4/24**	**Mon 9/16/24**	**Fri 9/5/25**		
328	**Sidewalk Walgreens to Big Island Poke - Sta 14+30.99 to 19+12.69**	**8 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 9/16/24**	**Wed 9/25/24**	**Mon 9/16/24**	**Fri 9/5/25**		
329	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	3 d	0 d	0 d	NA	NA	Mon 9/16/24	Wed 9/18/24	Mon 9/16/24	Wed 9/18/24	116,231,127,173,226,274,284,291,295	Pivetta - Earthwork
330	FRPCS - Sidewalk and Driveway Approaches	3 d	2 d	0 d	NA	NA	Thu 9/19/24	Mon 9/23/24	Mon 9/23/24	Wed 9/25/24	329	WCCI
331	Grade/Form/Pour - Curb Ramps/Install DWS - 2nd St. - Sta 19+64.04	2 d	232 d	23 d	NA	NA	Tue 9/24/24	Wed 9/25/24	Thu 9/4/25	Fri 9/5/25	330	WCCI
332	**Sidewalk Big Island Poke to SW Victoria St. - Sta 19+12.69 to 24+80**	**15 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 9/19/24**	**Wed 10/9/24**	**Thu 9/19/24**	**Fri 9/5/25**		
333	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	5 d	0 d	0 d	NA	NA	Thu 9/19/24	Wed 9/25/24	Thu 9/19/24	Wed 9/25/24	329	Pivetta - Earthwork
334	FRPCS - Sidewalk and Driveway Approaches	5 d	0 d	0 d	NA	NA	Thu 9/26/24	Wed 10/2/24	Thu 9/26/24	Wed 10/2/24	333,330	WCCI
335	Grade/Form/Pour - Curb Ramps/Install DWS - 2nd St. - Sta 20+08	5 d	222 d	13 d	NA	NA	Thu 10/3/24	Wed 10/9/24	Fri 8/29/25	Fri 9/5/25	334	WCCI
336	Grade/Form/Pour - Curb Ramps/Install DWS - Rainier/SW Victoria St. - Sta 24+44	2 d	225 d	16 d	NA	NA	Thu 10/3/24	Fri 10/4/24	Thu 9/4/25	Fri 9/5/25	334	WCCI
337	**Sidewalk - SW Victoria St. to Renton Ave Ext. - Sta 25+00 to 31+64.76**	**13 d**	**2 d**	**2 d**	**NA**	**NA**	**Thu 9/26/24**	**Mon 10/14/24**	**Mon 9/30/24**	**Fri 9/5/25**		
338	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	3 d	2 d	0 d	NA	NA	Thu 9/26/24	Mon 9/30/24	Mon 9/30/24	Wed 10/2/24	333	Pivetta - Earthwork
339	FRPCS - Sidewalk and Driveway Approaches	3 d	0 d	0 d	NA	NA	Thu 10/3/24	Mon 10/7/24	Thu 10/3/24	Mon 10/7/24	338,334	WCCI
340	Grade/Form/Pour - Curb Ramps/Install DWS - Rainier/SW Victoria St. - Sta 25+39.73	2 d	222 d	13 d	NA	NA	Tue 10/8/24	Wed 10/9/24	Thu 9/4/25	Fri 9/5/25	339	WCCI
341	Grade/Form/Pour - Curb Ramps/Install DWS - Midblock Crosswalk - Sta 25+47.49	5 d	0 d	0 d	NA	NA	Tue 10/8/24	Mon 10/14/24	Tue 10/8/24	Mon 10/14/24	339	WCCI
342	Grade/Form/Pour - Curb Ramps/Install DWS - Renton Ave. Ext. - Sta 31+40.67	2 d	222 d	13 d	NA	NA	Tue 10/8/24	Wed 10/9/24	Thu 9/4/25	Fri 9/5/25	339	WCCI
343	**Sidewalk - Renton Ave. Ext to End - Sta 32+30 to 42+80.28**	**17 d**	**5 d**	**5 d**	**NA**	**NA**	**Tue 10/1/24**	**Wed 10/23/24**	**Tue 10/8/24**	**Fri 9/5/25**		
344	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	5 d	5 d	0 d	NA	NA	Tue 10/1/24	Mon 10/7/24	Tue 10/8/24	Mon 10/14/24	338	Pivetta - Earthwork
345	FRPCS - Sidewalk and Driveway Approaches	5 d	0 d	0 d	NA	NA	Tue 10/15/24	Mon 10/21/24	Tue 10/15/24	Mon 10/21/24	339,341,344	WCCI
346	Grade/Form/Pour - Curb Ramps/Install DWS - Renton Ave. Ext. - Sta 32+30	2 d	212 d	3 d	NA	NA	Tue 10/22/24	Wed 10/23/24	Thu 9/4/25	Fri 9/5/25	345	WCCI
347	Grade/Form/Pour - Curb Ramps/Install DWS - Renton Ave Ext. - Sta 32+71.52 to 33+97.39	2 d	212 d	3 d	NA	NA	Tue 10/22/24	Wed 10/23/24	Thu 9/4/25	Fri 9/5/25	345	WCCI
348	Grade/Form/Pour - Curb Ramps/Install DWS - NW 3rd Pl - Sta 40+32.69 to 41+26.24	2 d	212 d	3 d	NA	NA	Tue 10/22/24	Wed 10/23/24	Thu 9/4/25	Fri 9/5/25	345	WCCI
349	**Concrete Switchback - Sta 37+14.35 to 37+34.20**	**20 d**	**190 d**	**190 d**	**NA**	**NA**	**Tue 10/8/24**	**Mon 11/4/24**	**Mon 7/21/25**	**Fri 8/15/25**		
350	Excavate/Place 4" Compacted CSBC	10 d	190 d	0 d	NA	NA	Tue 10/8/24	Mon 10/21/24	Mon 7/21/25	Fri 8/1/25	344	Pivetta - Earthwork
351	FRPCS Cement Concrete Switchback, Ramp, Stairs	10 d	190 d	0 d	NA	NA	Tue 10/22/24	Mon 11/4/24	Mon 8/4/25	Fri 8/15/25	350	WCCI
352	**Urban Design Features**	**45 d**	**190 d**	**190 d**	**NA**	**NA**	**Tue 11/5/24**	**Fri 1/17/25**	**Mon 8/18/25**	**Mon 10/20/25**		
353	Fabricate Handrails	40 d	190 d	0 d	NA	NA	Tue 11/5/24	Fri 1/10/25	Mon 8/18/25	Mon 10/13/25	351	Pivetta
354	Install Handrails and Fencing	5 d	190 d	187 d	NA	NA	Mon 1/13/25	Fri 1/17/25	Tue 10/14/25	Mon 10/20/25	351,353	Pivetta
355	**Roadway - Sta 13+95 to 42+80.28**	**27 d**	**61 d**	**61 d**	**NA**	**NA**	**Fri 9/27/24**	**Mon 11/4/24**	**Fri 1/3/25**	**Fri 9/12/25**		
356	**HMA**	**27 d**	**61 d**	**61 d**	**NA**	**NA**	**Fri 9/27/24**	**Mon 11/4/24**	**Fri 1/3/25**	**Fri 9/12/25**		
357	**HMA - Southbound Rainier & Renton Ave Ext - Sta 13+95 to 42+80**	**27 d**	**61 d**	**61 d**	**NA**	**NA**	**Fri 9/27/24**	**Mon 11/4/24**	**Fri 1/3/25**	**Fri 9/12/25**		
358	Grind Pavement	5 d	61 d	0 d	NA	NA	Fri 9/27/24	Thu 10/3/24	Fri 1/3/25	Thu 1/9/25	185,323,326	Becker Blacktop
359	Grade Base/Place Geotextile & CSBC	10 d	61 d	0 d	NA	NA	Tue 10/1/24	Mon 10/14/24	Tue 1/7/25	Tue 1/21/25	358SS+2 d	Pivetta - Earthwork
360	Prep T Cuts	10 d	72 d	11 d	NA	NA	Thu 10/3/24	Wed 10/16/24	Mon 1/27/25	Fri 2/7/25	359SS+2 d	Pivetta - Earthwork

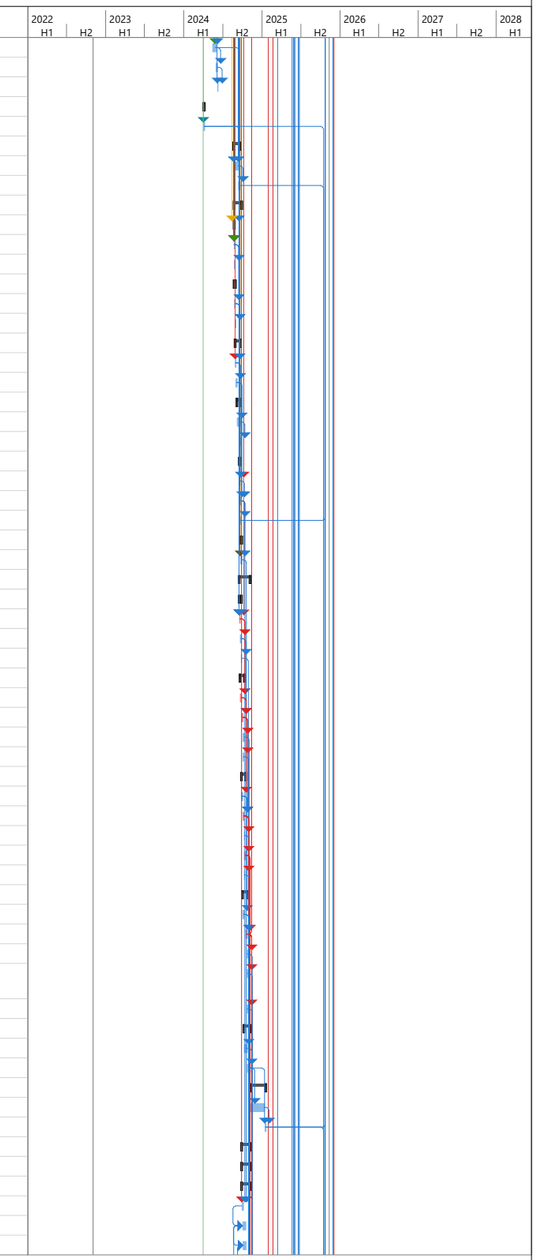

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
361	Place 8" HMA CL 1/2" PG 70-22 - New HMA Section/Trench Patch - Southbound Rainier Ave, Side Streets	5 d	61 d	0 d	NA	NA	Tue 10/22/24	Mon 10/28/24	Wed 1/29/25	Tue 2/4/25	360SS+2 d,365	Icon
362	Grade/Place CSBC/Place 4" HMA - Driveways	5 d	209 d	171 d	NA	NA	Tue 10/29/24	Mon 11/4/24	Mon 9/8/25	Fri 9/12/25	361,345,331,335,336,340,341,342,34€	Icon
363	**Concrete Panel Approaches (Rainier and 2nd St.) - Sta 18+57.89 to 18+92.89**	**12 d**	**61 d**	**61 d**	**NA**	**NA**	**Fri 10/4/24**	**Mon 10/21/24**	**Fri 1/10/25**	**Tue 1/28/25**		
364	Grade/Compact Subsurface and Place 2" CSBC - SB Rainier Ave. S.	2 d	61 d	0 d	NA	NA	Fri 10/4/24	Mon 10/7/24	Fri 1/10/25	Mon 1/13/25	359SS+3 d	Pivetta - Earthwork
365	Install 10" Concrete Panels - SB Rainier Ave. S.	10 d	61 d	0 d	NA	NA	Tue 10/8/24	Mon 10/21/24	Tue 1/14/25	Tue 1/28/25	364	WCCI
366												
367	**Stage 2 (East)**	**151 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 1/29/25**	**Wed 9/3/25**	**Wed 1/29/25**	**Mon 10/20/25**	**278**	
368	**Temporary Channelization and Signalization 12+12.5 to 43+63**	**5 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 1/29/25**	**Tue 2/4/25**	**Wed 1/29/25**	**Tue 2/4/25**		
369	Install Construction Channelization, Striping, Warning Signs - Shift Traffic to West Side of Rainier Ave.	5 d	0 d	0 d	NA	NA	Wed 1/29/25	Tue 2/4/25	Wed 1/29/25	Tue 2/4/25	236,237,361SS,278	SPM
370	Adjust and Modify Signals	5 d	0 d	0 d	NA	NA	Wed 1/29/25	Tue 2/4/25	Wed 1/29/25	Tue 2/4/25	369SS,278	Golden Gate
371	**Site Prep - Sta 12+12.5 to 42+07.42**	**10 d**	**69 d**	**69 d**	**NA**	**NA**	**Wed 2/5/25**	**Wed 2/19/25**	**Wed 5/14/25**	**Wed 5/28/25**		
372	Clear & Grub - Stage 2	5 d	69 d	0 d	NA	NA	Wed 2/5/25	Tue 2/11/25	Wed 5/14/25	Tue 5/20/25	369,370	Pivetta - Earthwork
373	Relocate Cable Railing and Posts	5 d	69 d	0 d	NA	NA	Wed 2/5/25	Tue 2/11/25	Wed 5/14/25	Tue 5/20/25	372SS	Pivetta - Earthwork
374	Complete Removals	5 d	69 d	0 d	NA	NA	Wed 2/12/25	Wed 2/19/25	Wed 5/21/25	Wed 5/28/25	372,373	Pivetta - Earthwork
375	**Sewer - Sta 25+02.65 to 28+55.98**	**9 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 2/5/25**	**Tue 2/18/25**	**Wed 2/5/25**	**Tue 2/18/25**		
376	**Sewer - Royal Orchid/Formula 1 Fast Lube to S. Tobin St. - Sta 25+02.65 to 28+48.03**	**8 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 2/5/25**	**Fri 2/14/25**	**Wed 2/5/25**	**Fri 2/14/25**		
377	Install New 8" Sewer and Manhole	6 d	0 d	0 d	NA	NA	Wed 2/5/25	Wed 2/12/25	Wed 2/5/25	Wed 2/12/25	369,370	Pivetta - Sewer
378	Install New Side Sewers	2 d	0 d	0 d	NA	NA	Thu 2/13/25	Fri 2/14/25	Thu 2/13/25	Fri 2/14/25	377	Pivetta - Sewer
379	**S. Tobin St. - Night/Crossing Sta 28+48.03 to 28+55.98**	**1 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 2/18/25**	**Tue 2/18/25**	**Tue 2/18/25**	**Tue 2/18/25**		
380	Install 12" Sewer	1 d	0 d	0 d	NA	NA	Tue 2/18/25	Tue 2/18/25	Tue 2/18/25	Tue 2/18/25	377,378	Pivetta - Sewer
381	**Storm Drainage - Sta 203+50 (S. 3rd) to 41+72.60 (Rainier)**	**66 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 2/19/25**	**Wed 5/21/25**	**Wed 2/19/25**	**Wed 5/21/25**		
382	**S. 3rd Street to Taco Time - Sta 203+50 to 200+79.67 (S. 3rd) & 13+50 to 17+63.44 (Rainier)**	**19 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 2/19/25**	**Mon 3/17/25**	**Wed 2/19/25**	**Mon 3/17/25**		
383	Install Drainage and Catch Basins	16 d	0 d	0 d	NA	NA	Wed 2/19/25	Wed 3/12/25	Wed 2/19/25	Wed 3/12/25	380	Pivetta - Sewer
384	Install Filterra Units	3 d	0 d	0 d	NA	NA	Thu 3/13/25	Mon 3/17/25	Thu 3/13/25	Mon 3/17/25	383	Pivetta - Sewer
385	**Storm Drainage - Night/Crossing - Sta 14+25.73**	**2 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 3/18/25**	**Wed 3/19/25**	**Tue 3/18/25**	**Wed 3/19/25**		
386	Install Drainage and Catch Basin	2 d	0 d	0 d	NA	NA	Tue 3/18/25	Wed 3/19/25	Tue 3/18/25	Wed 3/19/25	384	Pivetta - Sewer
387	**Royal Orchid to N of Airport Way - Sta 24+83.45 to 34+19.81**	**18 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 3/20/25**	**Mon 4/14/25**	**Thu 3/20/25**	**Mon 4/14/25**		
388	Install Drainage and Catch Basins	15 d	0 d	0 d	NA	NA	Thu 3/20/25	Wed 4/9/25	Thu 3/20/25	Wed 4/9/25	386	Pivetta - Sewer
389	Install Filterra Units	3 d	0 d	0 d	NA	NA	Thu 4/10/25	Mon 4/14/25	Thu 4/10/25	Mon 4/14/25	388	Pivetta - Sewer
390	**Storm Drainage - Night/Crossing - Sta 30+78.93**	**3 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 4/15/25**	**Thu 4/17/25**	**Tue 4/15/25**	**Thu 4/17/25**		
391	Install Drainage and Catch Basin	2 d	0 d	0 d	NA	NA	Tue 4/15/25	Wed 4/16/25	Tue 4/15/25	Wed 4/16/25	389	Pivetta - Sewer
392	Install Filterra Unit	1 d	0 d	0 d	NA	NA	Thu 4/17/25	Thu 4/17/25	Thu 4/17/25	Thu 4/17/25	391	Pivetta - Sewer
393	**Airport Way - Sta 33+17.81 to 601+64.04**	**6 d**	**0 d**	**0 d**	**NA**	**NA**	**Fri 4/18/25**	**Fri 4/25/25**	**Fri 4/18/25**	**Fri 4/25/25**		
394	Install Drainage and Catch Basins	5 d	0 d	0 d	NA	NA	Fri 4/18/25	Thu 4/24/25	Fri 4/18/25	Thu 4/24/25	392	Pivetta - Sewer
395	Install Filterra Units	1 d	0 d	0 d	NA	NA	Fri 4/25/25	Fri 4/25/25	Fri 4/25/25	Fri 4/25/25	394	Pivetta - Sewer
396	**N of Airport Way to S. of Nelson Pl. - Sta 36+15.83 to 38+57.60 - Night/Partial Stage 3**	**7 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 4/28/25**	**Tue 5/6/25**	**Mon 4/28/25**	**Tue 5/6/25**		
397	Install Drainage and Catch Basins	6 d	0 d	0 d	NA	NA	Mon 4/28/25	Mon 5/5/25	Mon 4/28/25	Mon 5/5/25	395	Pivetta - Sewer
398	Install Filterra Units	1 d	0 d	0 d	NA	NA	Tue 5/6/25	Tue 5/6/25	Tue 5/6/25	Tue 5/6/25	397	Pivetta - Sewer
399	**S. of Nelson Pl to End - Sta 37+91.23 to 41+72.60**	**11 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 5/7/25**	**Wed 5/21/25**	**Wed 5/7/25**	**Wed 5/21/25**		
400	Install Drainage and Catch Basins	8 d	0 d	0 d	NA	NA	Wed 5/7/25	Fri 5/16/25	Wed 5/7/25	Fri 5/16/25	398	Pivetta - Sewer
401	Install Filterra Units	3 d	0 d	0 d	NA	NA	Mon 5/19/25	Wed 5/21/25	Mon 5/19/25	Wed 5/21/25	400	Pivetta - Sewer
402	**Illumination - Sta 204+60 to 201+25, 133+50 to 42+08**	**146 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 2/5/25**	**Wed 9/3/25**	**Mon 4/7/25**	**Wed 9/3/25**		
403	**Decorative Illumination System**	**146 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 2/5/25**	**Wed 9/3/25**	**Mon 4/7/25**	**Wed 9/3/25**		
404	**Below Ground**	**33 d**	**42 d**	**42 d**	**NA**	**NA**	**Wed 2/5/25**	**Mon 3/24/25**	**Mon 4/7/25**	**Wed 5/21/25**		
405	Trench and Conduit	23 d	42 d	0 d	NA	NA	Wed 2/5/25	Mon 3/10/25	Mon 4/7/25	Wed 5/7/25	369	Golden Gate
406	Foundations	24 d	42 d	0 d	NA	NA	Wed 2/5/25	Tue 3/11/25	Mon 4/7/25	Thu 5/8/25	405SS	Golden Gate
407	Junction Boxes	9 d	42 d	0 d	NA	NA	Wed 3/12/25	Mon 3/24/25	Fri 5/9/25	Wed 5/21/25	406	Golden Gate
408	**Above Ground**	**56 d**	**0 d**	**0 d**	**NA**	**NA**	**Fri 6/13/25**	**Wed 9/3/25**	**Fri 6/13/25**	**Wed 9/3/25**		
409	Set Poles	31 d	0 d	0 d	NA	NA	Fri 6/13/25	Tue 7/29/25	Fri 6/13/25	Tue 7/29/25	406,436	Golden Gate
410	Install Lighting Wiring	20 d	0 d	0 d	NA	NA	Wed 7/30/25	Tue 8/26/25	Wed 7/30/25	Tue 8/26/25	407,409	Golden Gate
411	Test and Turn On	2 d	0 d	0 d	NA	NA	Wed 8/27/25	Thu 8/28/25	Wed 8/27/25	Thu 8/28/25	409,410	Golden Gate
412	Remove and Salvage Old Poles&Wiring	3 d	0 d	0 d	NA	NA	Fri 8/29/25	Wed 9/3/25	Fri 8/29/25	Wed 9/3/25	411	Golden Gate
413	**Walls - Sta 18+53.50 to 33+39.60**	**25 d**	**68 d**	**68 d**	**NA**	**NA**	**Tue 3/25/25**	**Mon 4/28/25**	**Tue 7/1/25**	**Mon 10/20/25**		
414	**Wall 3 - CCFW and Modular Block Wall - Sta 300+54.06 to 301+10.11**	**15 d**	**68 d**	**68 d**	**NA**	**NA**	**Tue 3/25/25**	**Mon 4/14/25**	**Tue 7/1/25**	**Tue 7/22/25**		
415	Construct Concrete Fill Wall - Sta 17+53.50 to 18+48.48	5 d	68 d	0 d	NA	NA	Tue 3/25/25	Mon 3/31/25	Tue 7/1/25	Tue 7/8/25	407,369	WCCI
416	Construct Modular Block Wall - Sta 300+54.05 to 301+10.11	10 d	68 d	0 d	NA	NA	Tue 4/1/25	Mon 4/14/25	Wed 7/9/25	Tue 7/22/25	415	Key West
417	**Wall 4 - Modular Block Wall - Sta 21+11.76 to 21+59.62**	**5 d**	**68 d**	**68 d**	**NA**	**NA**	**Tue 4/15/25**	**Mon 4/21/25**	**Wed 7/23/25**	**Tue 7/29/25**		
418	Construct Modular Block Wall - Sta 21+11.76 to 21+59.62	5 d	68 d	30 d	NA	NA	Tue 4/15/25	Mon 4/21/25	Wed 7/23/25	Tue 7/29/25	416	Key West
419	**Gateway Wall B - Sta 33+39.60 to 600+57.12**	**20 d**	**68 d**	**68 d**	**NA**	**NA**	**Tue 4/1/25**	**Mon 4/28/25**	**Wed 7/9/25**	**Mon 10/20/25**		
420	Construct Gateway Wall B	15 d	68 d	0 d	NA	NA	Tue 4/1/25	Mon 4/21/25	Wed 7/9/25	Tue 7/29/25	415	WCCI

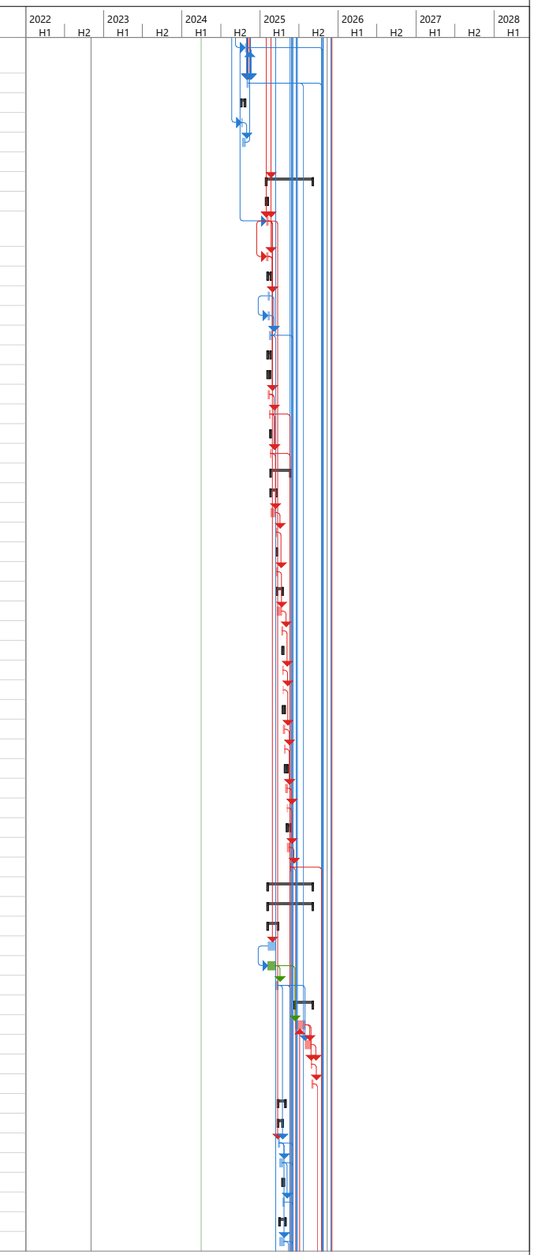

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
421	Install Decorative Cutouts and Skate Deterrent - Gateway Wall B	5 d	121 d	118 d	NA	NA	Tue 4/22/25	Mon 4/28/25	Tue 10/14/25	Mon 10/20/25	420	WCCI
422	**Curb and Gutter - Sta 204+63.59 to 42+07.42**	**17 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 5/22/25**	**Mon 6/16/25**	**Thu 5/22/25**	**Wed 8/13/25**		
423	**Curb and Gutter - S. 3rd St. to S. 2nd St. - Sta 204+63.59 to 301+09.32**	**8 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 5/22/25**	**Tue 6/3/25**	**Thu 5/22/25**	**Tue 6/3/25**		
424	Grade/Prep Base/Place CSBC	4 d	0 d	0 d	NA	NA	Thu 5/22/25	Wed 5/28/25	Thu 5/22/25	Wed 5/28/25	401,173,378,380,407	Pivetta - Earthwork
425	Form and Pour Curb and Gutter	4 d	0 d	0 d	NA	NA	Thu 5/29/25	Tue 6/3/25	Thu 5/29/25	Tue 6/3/25	424	WCCI
426	**Curb and Gutter - S. 2nd St. to S. Tobin St. - Sta 19+57.82 to 28+61.93**	**6 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 5/29/25**	**Thu 6/5/25**	**Fri 5/30/25**	**Thu 6/5/25**		
427	Grade/Prep Base/Place CSBC	2 d	1 d	0 d	NA	NA	Thu 5/29/25	Fri 5/30/25	Fri 5/30/25	Mon 6/2/25	424,180,176	Pivetta - Earthwork
428	Form and Pour Curb and Gutter	2 d	0 d	0 d	NA	NA	Wed 6/4/25	Thu 6/5/25	Wed 6/4/25	Thu 6/5/25	425,427	WCCI
429	**Curb and Gutter - S. Tobin St. to Airport Way - Sta 28+61.93 to 604+36.35**	**11 d**	**1 d**	**1 d**	**NA**	**NA**	**Mon 6/2/25**	**Mon 6/16/25**	**Tue 6/3/25**	**Wed 8/13/25**		
430	Grade/Prep Base/Place CSBC	2 d	1 d	0 d	NA	NA	Mon 6/2/25	Tue 6/3/25	Tue 6/3/25	Wed 6/4/25	427,122	Pivetta - Earthwork
431	Form and Pour Curb and Gutter	2 d	0 d	0 d	NA	NA	Fri 6/6/25	Mon 6/9/25	Fri 6/6/25	Mon 6/9/25	430,428	WCCI
432	**Islands - Sta 31+86.30 to 601+03.49**	**5 d**	**40 d**	**40 d**	**NA**	**NA**	**Tue 6/10/25**	**Mon 6/16/25**	**Thu 8/7/25**	**Wed 8/13/25**		
433	Grade/Place CSBC/Place Island 1 - Airport Way	5 d	40 d	0 d	NA	NA	Tue 6/10/25	Mon 6/16/25	Thu 8/7/25	Wed 8/13/25	431	Pivetta - Earthwork
434	**Curb and Gutter - Airport Way to End - Sta 603+57.87 to 42+07.42**	**7 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 6/4/25**	**Thu 6/12/25**	**Thu 6/5/25**	**Thu 6/12/25**		
435	Grade/Prep Base/Place CSBC	3 d	1 d	1 d	NA	NA	Wed 6/4/25	Fri 6/6/25	Thu 6/5/25	Mon 6/9/25	430	Pivetta - Earthwork
436	Form and Pour Curb and Gutter	3 d	0 d	0 d	NA	NA	Tue 6/10/25	Thu 6/12/25	Tue 6/10/25	Thu 6/12/25	431,435	WCCI
437	**Sidewalk - Sta 204+63.59 to 42+07.42**	**37 d**	**38 d**	**38 d**	**NA**	**NA**	**Wed 6/4/25**	**Mon 7/28/25**	**Wed 7/30/25**	**Mon 10/20/25**		
438	**Sidewalk - S. 3rd St. to S. 2nd St. - Sta 204+63.59 to 301+09.32**	**17 d**	**38 d**	**38 d**	**NA**	**NA**	**Wed 6/4/25**	**Fri 6/27/25**	**Wed 7/30/25**	**Thu 8/28/25**		
439	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	5 d	38 d	0 d	NA	NA	Wed 6/4/25	Tue 6/10/25	Wed 7/30/25	Tue 8/5/25	151,425,374,415,416,418,420,470	Pivetta - Earthwork
440	FRPCS - Sidewalk and Driveway Approaches	8 d	38 d	0 d	NA	NA	Fri 6/13/25	Wed 6/25/25	Fri 8/8/25	Tue 8/19/25	439SS+2 d,436	WCCI
441	Grade/Form/Pour - Curb Ramps/Install DWS - S. 3rd St. - Sta 12+12.51 to 201+45.07	2 d	43 d	5 d	NA	NA	Thu 6/26/25	Fri 6/27/25	Wed 8/27/25	Thu 8/28/25	440	WCCI
442	Grade/Form/Pour - Curb Ramps/Install DWS - S. 3rd St. - Sta 200+78.57 to 14+00.41	2 d	43 d	5 d	NA	NA	Thu 6/26/25	Fri 6/27/25	Wed 8/27/25	Thu 8/28/25	440	WCCI
443	Grade/Form/Pour - Curb Ramps/Install DWS - S. 2nd St. - Sta 18+48.51 to 19+08.79	2 d	43 d	5 d	NA	NA	Thu 6/26/25	Fri 6/27/25	Wed 8/27/25	Thu 8/28/25	440	WCCI
444	**Sidewalk - S. 2nd St. to S. Tobin St. - Sta 19+57.82 to 28+61.93**	**17 d**	**38 d**	**38 d**	**NA**	**NA**	**Wed 6/11/25**	**Mon 7/7/25**	**Wed 8/6/25**	**Mon 10/20/25**		
445	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	5 d	38 d	0 d	NA	NA	Wed 6/11/25	Tue 6/17/25	Wed 8/6/25	Tue 8/12/25	439	Pivetta - Earthwork
446	FRPCS - Sidewalk and Driveway Approaches	5 d	38 d	0 d	NA	NA	Thu 6/26/25	Wed 7/2/25	Wed 8/20/25	Tue 8/26/25	445,440,451	WCCI
447	Grade/Form/Pour - Curb Ramps/Install DWS - S. 2nd St. - Sta 19+55.68 to 20+08.13	2 d	38 d	0 d	NA	NA	Thu 7/3/25	Mon 7/7/25	Wed 8/27/25	Thu 8/28/25	446	WCCI
448	Grade/Form/Pour - Curb Ramps/Install DWS - Midblock Crosswalk - Sta 25+40.51 to 25+47.25	2 d	38 d	0 d	NA	NA	Thu 7/3/25	Mon 7/7/25	Wed 8/27/25	Thu 8/28/25	446	WCCI
449	Grade/Form/Pour - Curb Ramps/Install DWS - S. Tobin St. - Sta 27+93.39 to 500+74.79	2 d	38 d	0 d	NA	NA	Thu 7/3/25	Mon 7/7/25	Wed 8/27/25	Thu 8/28/25	446	WCCI
450	**Bus Shelter - Sta 24+59.90**	**6 d**	**38 d**	**38 d**	**NA**	**NA**	**Wed 6/18/25**	**Thu 6/26/25**	**Wed 8/13/25**	**Mon 10/20/25**		
451	FRPCS Bus Shelter Footings	5 d	38 d	0 d	NA	NA	Wed 6/18/25	Wed 6/25/25	Wed 8/13/25	Tue 8/19/25	445	WCCI
452	Install Bus Shelter	1 d	80 d	77 d	NA	NA	Thu 6/26/25	Thu 6/26/25	Mon 10/20/25	Mon 10/20/25	451	Pivetta
453	**Sidewalk - S. Tobin St. to Airport Way**	**5 d**	**39 d**	**39 d**	**NA**	**NA**	**Wed 6/18/25**	**Wed 6/25/25**	**Thu 8/14/25**	**Fri 8/22/25**		
454	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	4 d	39 d	0 d	NA	NA	Wed 6/18/25	Tue 6/24/25	Thu 8/14/25	Tue 8/19/25	445	Pivetta - Earthwork
455	FRPCS - Sidewalk and Driveway Approaches	4 d	41 d	2 d	NA	NA	Fri 6/20/25	Wed 6/25/25	Tue 8/19/25	Fri 8/22/25	454SS+1 d	WCCI
456	**Shared Use Path - Airport Way to Sta 38+80**	**27 d**	**39 d**	**39 d**	**NA**	**NA**	**Wed 6/18/25**	**Mon 7/28/25**	**Thu 8/14/25**	**Mon 10/20/25**		
457	Grade/Prep Base/Place CSBC - Shared Use Path	5 d	39 d	0 d	NA	NA	Wed 6/18/25	Wed 6/25/25	Thu 8/14/25	Wed 8/20/25	454SS	Pivetta - Earthwork
458	Place HMA - Shared Use Path	5 d	62 d	59 d	NA	NA	Thu 7/17/25	Wed 7/23/25	Tue 10/14/25	Mon 10/20/25	457,479,461	WCCI
459	**Concrete Switchback - Sta 35+36.63 to 35+68.13**	**23 d**	**59 d**	**59 d**	**NA**	**NA**	**Wed 6/25/25**	**Mon 7/28/25**	**Tue 9/23/25**	**Mon 10/20/25**		
460	Excavate/Place 4" Compacted CSBC	5 d	62 d	0 d	NA	NA	Wed 6/25/25	Tue 7/1/25	Tue 9/23/25	Mon 9/29/25	454	Pivetta - Earthwork
461	FRPCS Cement Concrete Switchback, Ramp, Stairs	10 d	62 d	0 d	NA	NA	Wed 7/2/25	Wed 7/16/25	Tue 9/30/25	Mon 10/13/25	460	WCCI
462	Install Handrails and Fencing	5 d	59 d	56 d	NA	NA	Tue 7/22/25	Mon 7/28/25	Tue 10/14/25	Mon 10/20/25	461,473	WCCI
463	**Sidewalk - Airport Way to End - 603+57.87 to 42+07.42**	**6 d**	**39 d**	**39 d**	**NA**	**NA**	**Thu 6/26/25**	**Thu 7/3/25**	**Thu 8/21/25**	**Thu 8/28/25**		
464	Grade/Prep Base/Place CSBC - Sidewalk and Driveway Approaches	2 d	39 d	0 d	NA	NA	Thu 6/26/25	Fri 6/27/25	Thu 8/21/25	Fri 8/22/25	457	Pivetta - Earthwork
465	FRPCS - Sidewalk and Driveway Approaches	2 d	39 d	0 d	NA	NA	Mon 6/30/25	Tue 7/1/25	Mon 8/25/25	Tue 8/26/25	455,464	WCCI
466	Grade/Form/Pour - Curb Ramps/Install DWS - S. Tobin St. - Sta 500+87.95 to 500+39.28	2 d	39 d	1 d	NA	NA	Wed 7/2/25	Thu 7/3/25	Wed 8/27/25	Thu 8/28/25	465	WCCI
467	Grade/Form/Pour - Curb Ramps/Install DWS - Airport Way - Sta 31+31.67 to 32+15.90	2 d	39 d	1 d	NA	NA	Wed 7/2/25	Thu 7/3/25	Wed 8/27/25	Thu 8/28/25	465	WCCI
468	Grade/Form/Pour - Curb Ramps/Install DWS - Airport Way - Sta 33+20.23 to 33+65.12	2 d	39 d	0 d	NA	NA	Wed 7/2/25	Thu 7/3/25	Wed 8/27/25	Thu 8/28/25	465	WCCI
469	**Urban Design Features**	**105 d**	**59 d**	**59 d**	**NA**	**NA**	**Thu 2/20/25**	**Mon 7/21/25**	**Mon 7/28/25**	**Mon 10/13/25**		
470	Drill Foundations for Decorative Trellis	2 d	109 d	71 d	NA	NA	Thu 2/20/25	Fri 2/21/25	Mon 7/28/25	Tue 7/29/25	374	Pivetta
471	Install Trellis	5 d	59 d	0 d	NA	NA	Mon 7/7/25	Fri 7/11/25	Mon 9/29/25	Fri 10/3/25	468	Pivetta
472	Install Trash Receptacles and Benches	1 d	59 d	0 d	NA	NA	Mon 7/14/25	Mon 7/14/25	Mon 10/6/25	Mon 10/6/25	468,471	Pivetta
473	Install Fence	5 d	59 d	0 d	NA	NA	Tue 7/15/25	Mon 7/21/25	Tue 10/7/25	Mon 10/13/25	468,472	Pivetta
474	**Roadway - Sta 12+12.5 to 43+63**	**23 d**	**40 d**	**40 d**	**NA**	**NA**	**Tue 6/17/25**	**Mon 7/21/25**	**Thu 8/14/25**	**Mon 10/20/25**		
475	**HMA - Northbound Rainier & Airport Way - Sta 12+12.5 to 43+63**	**23 d**	**38 d**	**38 d**	**NA**	**NA**	**Tue 6/17/25**	**Mon 7/21/25**	**Thu 8/14/25**	**Fri 9/12/25**		
476	Grind Pavement	5 d	40 d	0 d	NA	NA	Tue 6/17/25	Tue 6/24/25	Thu 8/14/25	Wed 8/20/25	436,433	Becker Blacktop
477	Grade Base/Place Geotextile & CSBC	10 d	40 d	0 d	NA	NA	Fri 6/20/25	Thu 7/3/25	Mon 8/18/25	Fri 8/29/25	165,173,476SS+2 d	Pivetta - Earthwork
478	Prep T Cuts	10 d	40 d	0 d	NA	NA	Tue 6/24/25	Tue 7/8/25	Wed 8/20/25	Wed 9/3/25	477SS+2 d	Pivetta - Earthwork
479	Place 8" HMA CL 1/2" PG 70-22 - New HMA Section/Trench Patch - Southbound Rainier Ave, Side Streets	5 d	40 d	0 d	NA	NA	Thu 6/26/25	Wed 7/2/25	Fri 8/22/25	Thu 8/28/25	478SS+2 d	Icon
480	Grade/Place CSBC/Place 4" HMA - Driveways	10 d	38 d	0 d	NA	NA	Tue 7/8/25	Mon 7/21/25	Fri 8/29/25	Fri 9/12/25	479,441,442,443,447,448,449,466,467	Icon

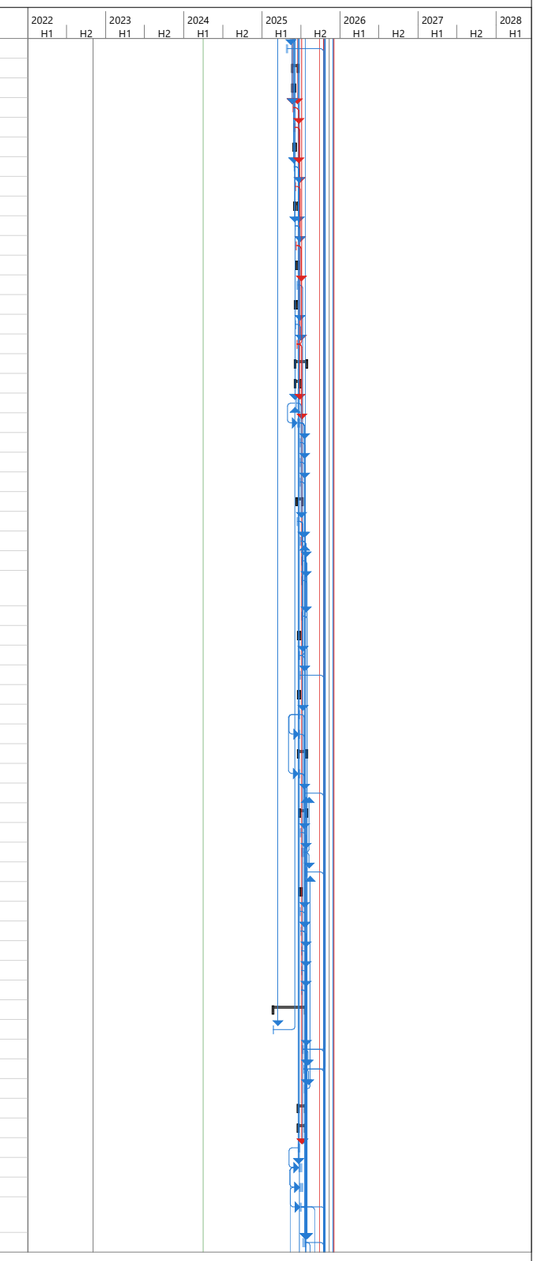

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress

ID	Task Name	Duration	Total Slack	Free Slack	Actual Start	Actual Finish	Early Start	Early Finish	Late Start	Late Finish	Predecessors	Text2
481	**Concrete Panel Approaches (Rainier and 2nd St.) - Sta 18+57.89 to 18+92.89**	**7 d**	**42 d**	**42 d**	**NA**	**NA**	**Wed 6/25/25**	**Thu 7/3/25**	**Mon 8/25/25**	**Wed 9/3/25**		
482	Grade/Compact Subsurface and Place 2" CSBC - SB Rainier Ave. S.	2 d	42 d	0 d	NA	NA	Wed 6/25/25	Thu 6/26/25	Mon 8/25/25	Tue 8/26/25	477SS+3 d,151	Pivetta - Earthwork
483	Install 10" Concrete Panels - SB Rainier Ave. S.	5 d	42 d	42 d	NA	NA	Fri 6/27/25	Thu 7/3/25	Wed 8/27/25	Wed 9/3/25	482	WCCI
484	**Dual Faced Slope Mountable Curb - Airport Way - Sta 600+90 to 603+45**	**7 d**	**69 d**	**69 d**	**NA**	**NA**	**Thu 7/3/25**	**Mon 7/14/25**	**Fri 10/10/25**	**Mon 10/20/25**		
485	**S. 3rd St. - Sta to 200+62 to 201+55**	**5 d**	**69 d**	**69 d**	**NA**	**NA**	**Thu 7/3/25**	**Thu 7/10/25**	**Fri 10/10/25**	**Fri 10/17/25**		
486	FRPCS - Dual Faced Sloped Mountable Traffic Curb - S. 3rd St.	4 d	69 d	0 d	NA	NA	Thu 7/3/25	Wed 7/9/25	Fri 10/10/25	Wed 10/15/25	479	SPM
487	Install Curb Mounted Delineator Posts - S. 3rd St.	1 d	70 d	1 d	NA	NA	Thu 7/10/25	Thu 7/10/25	Fri 10/17/25	Fri 10/17/25	486	SPM
488	**Airport Way - Sta 600+90 to 603+45**	**3 d**	**69 d**	**69 d**	**NA**	**NA**	**Thu 7/10/25**	**Mon 7/14/25**	**Thu 10/16/25**	**Mon 10/20/25**		
489	FRPCS - Dual Faced Sloped Mountable Traffic Curb - Airport Way	2 d	69 d	0 d	NA	NA	Thu 7/10/25	Fri 7/11/25	Thu 10/16/25	Fri 10/17/25	486	SPM
490	Install Curb Mounted Delineator Posts - Airport Way	1 d	69 d	69 d	NA	NA	Mon 7/14/25	Mon 7/14/25	Mon 10/20/25	Mon 10/20/25	489,487	SPM
491												
492	**Stage 3 (Median)**	**48 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 9/4/25**	**Mon 11/10/25**	**Thu 9/4/25**	**Mon 11/10/25**		
493	**Temporary Channelization and Signalization - 14+05 to 40+15**	**2 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 9/4/25**	**Fri 9/5/25**	**Thu 9/4/25**	**Fri 9/5/25**		
494	Install Const. Channelization & Shift Traffic to Outside Lanes - Rainier Ave S.	2 d	0 d	0 d	NA	NA	Thu 9/4/25	Fri 9/5/25	Thu 9/4/25	Fri 9/5/25	412,483,479	Pivetta
495	Adjust Signal Heads and Cameras	2 d	0 d	0 d	NA	NA	Thu 9/4/25	Fri 9/5/25	Thu 9/4/25	Fri 9/5/25	494SS	Golden Gate
496	**Site Prep - Sta 14+05 to 40+15**	**5 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 9/8/25**	**Fri 9/12/25**	**Mon 9/8/25**	**Fri 9/12/25**		
497	Sawcut and Remove Pavement in Median	5 d	0 d	0 d	NA	NA	Mon 9/8/25	Fri 9/12/25	Mon 9/8/25	Fri 9/12/25	494,495	Pivetta
498	**Roadway - Sta 14+05 to 40+40**	**31 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 9/15/25**	**Mon 10/27/25**	**Mon 9/15/25**	**Mon 10/27/25**		
499	**Median 1 - Sta 14+05 to 18+44.96**	**20 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 9/15/25**	**Fri 10/10/25**	**Mon 9/15/25**	**Wed 10/15/25**		
500	Grade Base/Place CSBC/FRPCS Median 1 Curb	5 d	0 d	0 d	NA	NA	Mon 9/15/25	Fri 9/19/25	Mon 9/15/25	Fri 9/19/25	497,539SS	Pivetta - Earthwork
501	Install River Rock Treatment	5 d	3 d	0 d	NA	NA	Mon 9/22/25	Fri 9/26/25	Thu 9/25/25	Wed 10/1/25	500	WCCI
502	Install Bioretention Planter Area	5 d	3 d	0 d	NA	NA	Mon 9/29/25	Fri 10/3/25	Thu 10/2/25	Wed 10/8/25	501	Coria
503	Install Plants	5 d	3 d	0 d	NA	NA	Mon 10/6/25	Fri 10/10/25	Thu 10/9/25	Wed 10/15/25	502	Pivetta
504	Adjust Monument Case and Cover to FG	1 d	11 d	11 d	NA	NA	Mon 9/22/25	Mon 9/22/25	Tue 10/7/25	Tue 10/7/25	500	Pivetta
505	**Median 2 - Sta 19+65**	**7 d**	**0 d**	**0 d**	**NA**	**NA**	**Mon 9/22/25**	**Tue 9/30/25**	**Mon 9/22/25**	**Tue 10/7/25**		
506	Grade Base/Place CSBC/FRPCS Median Curb 2	3 d	0 d	0 d	NA	NA	Mon 9/22/25	Wed 9/24/25	Mon 9/22/25	Wed 9/24/25	500	Pivetta - Earthwork
507	Install River Rock Treatment	2 d	5 d	1 d	NA	NA	Mon 9/29/25	Tue 9/30/25	Mon 10/6/25	Tue 10/7/25	506,501	WCCI
508	**Median 3 - Sta 23+40 to 25+50**	**15 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 9/25/25**	**Wed 10/15/25**	**Thu 9/25/25**	**Mon 10/20/25**		
509	Grade Base/Place CSBC/FRPCS Median Curb 3	3 d	0 d	0 d	NA	NA	Thu 9/25/25	Mon 9/29/25	Thu 9/25/25	Mon 9/29/25	506,539SS	Pivetta - Earthwork
510	Install Midblock Crosswalk and DWS	2 d	4 d	0 d	NA	NA	Tue 9/30/25	Wed 10/1/25	Mon 10/6/25	Tue 10/7/25	509	WCCI
511	Install River Rock Treatment	3 d	4 d	0 d	NA	NA	Thu 10/2/25	Mon 10/6/25	Wed 10/8/25	Fri 10/10/25	507,510	WCCI
512	Install Bioretention Planter Area	3 d	4 d	1 d	NA	NA	Tue 10/7/25	Thu 10/9/25	Mon 10/13/25	Wed 10/15/25	511	Coria
513	Install Plants	3 d	3 d	0 d	NA	NA	Mon 10/13/25	Wed 10/15/25	Thu 10/16/25	Mon 10/20/25	503,512	Coria
514	Install Root Barrier	3 d	3 d	0 d	NA	NA	Mon 10/13/25	Wed 10/15/25	Thu 10/16/25	Mon 10/20/25	513SS	Coria
515	**Median 4 - Sta 25+50 to 31+65.38**	**6 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 9/25/25**	**Thu 10/2/25**	**Thu 9/25/25**	**Fri 10/3/25**		
516	Grade Base/Place CSBC/FRPCS Median Curb 4	3 d	0 d	0 d	NA	NA	Thu 9/25/25	Mon 9/29/25	Thu 9/25/25	Mon 9/29/25	509SS,539SS	Piveta - Earthwork
517	Install River Rock Treatment	3 d	1 d	0 d	NA	NA	Tue 9/30/25	Thu 10/2/25	Wed 10/1/25	Fri 10/3/25	516	WCCI
518	**Median 5 - Sta 38+39.71 to 40+12.21**	**5 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 9/30/25**	**Mon 10/6/25**	**Tue 9/30/25**	**Tue 10/7/25**		
519	Grade Base/Place CSBC/FRPCS Median Curb 5	3 d	0 d	0 d	NA	NA	Tue 9/30/25	Thu 10/2/25	Tue 9/30/25	Thu 10/2/25	516	Piveta - Earthwork
520	Install River Rock Treatment	2 d	1 d	1 d	NA	NA	Fri 10/3/25	Mon 10/6/25	Mon 10/6/25	Tue 10/7/25	517,519	WCCI
521	**Traffic Mounted Curb - Sta 20+25 to 23+40, 33+50 to 38+39.71**	**6 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 9/30/25**	**Tue 10/7/25**	**Tue 9/30/25**	**Tue 10/7/25**		
522	Install Traffic Mounted Curb North of S. 2nd Street to Median 3	3 d	0 d	0 d	NA	NA	Tue 9/30/25	Thu 10/2/25	Tue 9/30/25	Thu 10/2/25	509	SPM
523	Install Traffic Mounted Curb North of Airport Way to Median 5	3 d	0 d	0 d	NA	NA	Fri 10/3/25	Tue 10/7/25	Fri 10/3/25	Tue 10/7/25	522,519	SPM
524	**HMA Paving - Sta 14+05 to 42+10**	**14 d**	**0 d**	**0 d**	**NA**	**NA**	**Wed 10/8/25**	**Mon 10/27/25**	**Wed 10/8/25**	**Mon 10/27/25**		
525	Grade Base/Place Geotextile & CSBC - New HMA Southbound Rainier	5 d	0 d	0 d	NA	NA	Wed 10/8/25	Tue 10/14/25	Wed 10/8/25	Tue 10/14/25	523,504,520	Pivetta - Earthwork
526	Place HMA to Curb - Southbound Rainier	2 d	10 d	10 d	NA	NA	Fri 10/10/25	Mon 10/13/25	Fri 10/24/25	Mon 10/27/25	525SS+2 d	Icon
527	Grade Base/Place Geotextile & CSBC - New HMA Section Northbound Rainier	5 d	0 d	0 d	NA	NA	Wed 10/15/25	Tue 10/21/25	Wed 10/15/25	Tue 10/21/25	525	Pivetta - Earthwork
528	Place HMA to Curb - Northbound Rainier	2 d	0 d	0 d	NA	NA	Fri 10/17/25	Mon 10/20/25	Fri 10/17/25	Mon 10/20/25	527SS+2 d	Icon
529	Place 4" Fiber Reinforced Asphalt Concrete (FRAC) - Project Wide	5 d	0 d	0 d	NA	NA	Tue 10/21/25	Mon 10/27/25	Tue 10/21/25	Mon 10/27/25	361,479,490,528	Icon
530	**Final Channelization and Striping**	**10 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 10/28/25**	**Mon 11/10/25**	**Tue 10/28/25**	**Mon 11/10/25**		
531	**Channelization and Striping - Southbound Rainier Ave - Sta 12+70.9 to 42+87.1**	**5 d**	**0 d**	**0 d**	**NA**	**NA**	**Tue 10/28/25**	**Mon 11/3/25**	**Tue 10/28/25**	**Mon 11/3/25**		
532	Install Striping, Arrows, Blue Hydrant Markers	2 d	0 d	0 d	NA	NA	Tue 10/28/25	Wed 10/29/25	Tue 10/28/25	Wed 10/29/25	526,529	SPM
533	Install Signs	5 d	0 d	0 d	NA	NA	Tue 10/28/25	Mon 11/3/25	Tue 10/28/25	Mon 11/3/25	532SS	Pivetta
534	**Channelization and Striping - Northbound Rainier Ave - Sta 12+70.9 to 42+80.29**	**8 d**	**0 d**	**0 d**	**NA**	**NA**	**Thu 10/30/25**	**Mon 11/10/25**	**Tue 11/4/25**	**Mon 11/10/25**		
535	Install Striping, Arrows, Blue Hydrant Markers	2 d	3 d	3 d	NA	NA	Thu 10/30/25	Fri 10/31/25	Tue 11/4/25	Wed 11/5/25	532,528	SPM
536	Install Signs	5 d	0 d	0 d	NA	NA	Tue 11/4/25	Mon 11/10/25	Tue 11/4/25	Mon 11/10/25	533,535SS	Pivetta
537												
538	**Landscaping and Irrigation**	**76 d**	**3 d**	**3 d**	**NA**	**NA**	**Tue 7/22/25**	**Wed 11/5/25**	**Mon 9/15/25**	**Mon 11/10/25**		
539	Install Irrigation	15 d	38 d	38 d	NA	NA	Tue 7/22/25	Mon 8/11/25	Mon 9/15/25	Fri 10/3/25	362,480	Coria
540	Install Landscaping	15 d	3 d	3 d	NA	NA	Thu 10/16/25	Wed 11/5/25	Tue 10/21/25	Mon 11/10/25	514,539,362,480,401,421,452,472,307	Coria

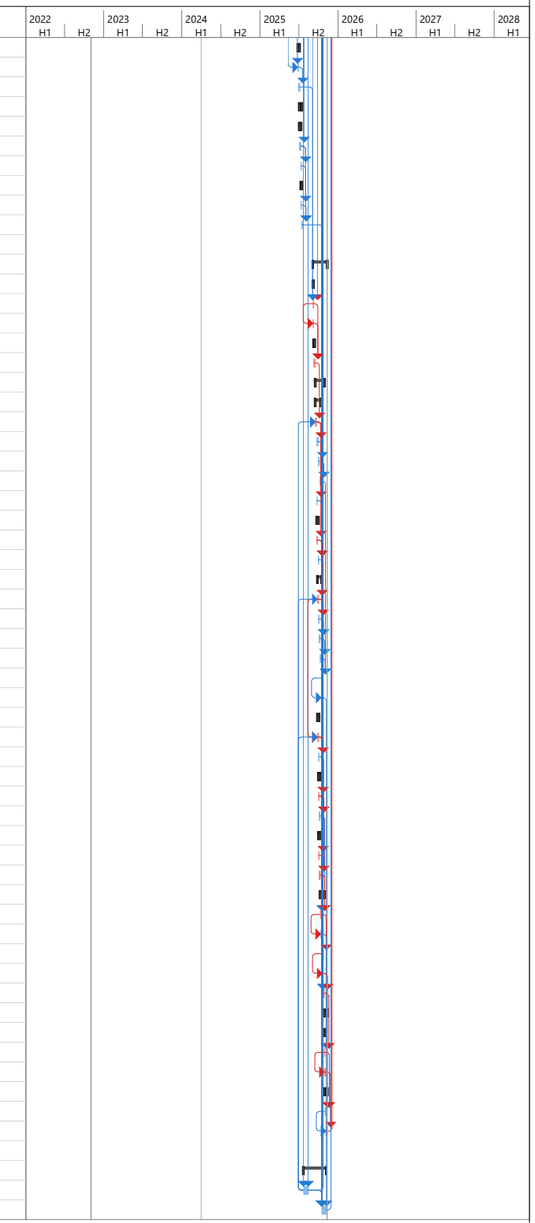

Project: Rainier Ave S Corridor Improvements - Phase 4 Project
City of Renton Project Number: CAG-22-163
Date: Mon 4/1/24

Task | Split | Milestone | Summary | Project Summary | Inactive Task | Inactive Milestone | Inactive Summary | Manual Task | Duration-only | Manual Summary Rollup | Manual Summary | Start-only | Finish-only | External Tasks | External Milestone | Deadline | Critical | Critical Split | Progress | Manual Progress
